


*Quote of the week: "A dream doesn't become reality through magic; it takes sweat, determination, and hardwork."*

## Project: Toomer ES Additions and Modification


Week Ending: February 2, 2023

### THIS WEEK:

- Hanging drywall at CMU top outs at all areas is complete
- Begin roofing at the new addition
- Continue MEP overhead rough in areas 1, 2 and 3
- Completed air barrier throughout
- Begin ceiling grid installation on the second floor of area 3
- Completed sanitary sewer tie-in at the west side of the project
- Begin storefront installation at Area 3
- Completed drywall finishing in area 3.
- Set all roof mounted HVAC units
- Begin soffit framing in the lobby area



*Begin installing new glass and storefront in area 3*

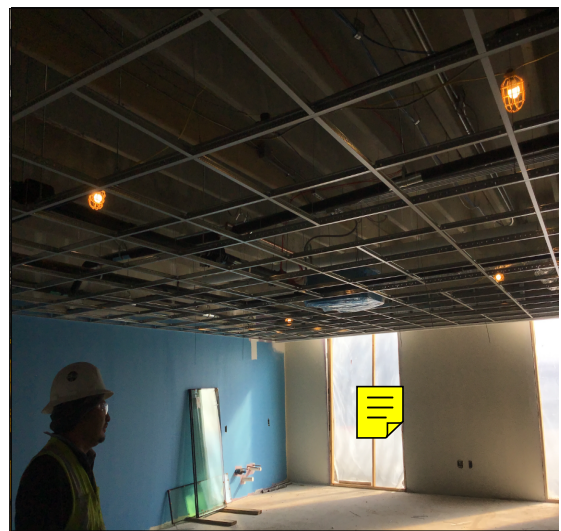

*Begin ceiling grid install on the 2nd floor of area 3*



*Begin installing coping at the roof.*



*All roof mounted HVAC units are set.*

### **NEXT WEEK – February 5 - February 9**

- Complete all foam insulation
- Continue painting drywall and CMU
- Complete all soffit framing
- Complete sanitary sewer system
- Install grease traps after existing storm line is re-routed
- Begin rooftop HVAC equipment hookups

### **SCHEDULED DATE OF SUBSTANTIAL COMPLETION**

- June 30, 2024

### **Final Completion**

- June 30, 2024

### **PREPARED BY:**

Jahaziel Lee, Carroll Daniel Construction Co.
