


Quote of the week: "Don't limit your challenges, challenge your limits."

Project: Toomer ES Additions and Modification


Week Ending: December 15, 2023

THIS WEEK:

- Installed new storm water system
- CMU walls in area 3 level 1 have been primed and coated
- Completed CMU walls in area 2
- Completed CMU wall construction in the cafeteria area
- Slab on grade pour is complete for the new security vestibule addition.
- Continue to install in wall insulation
- Continue interior drywall cover up in area 3
- Continue prepping to install kitchen grease traps




New security vestibule additions has poured and ready for steel

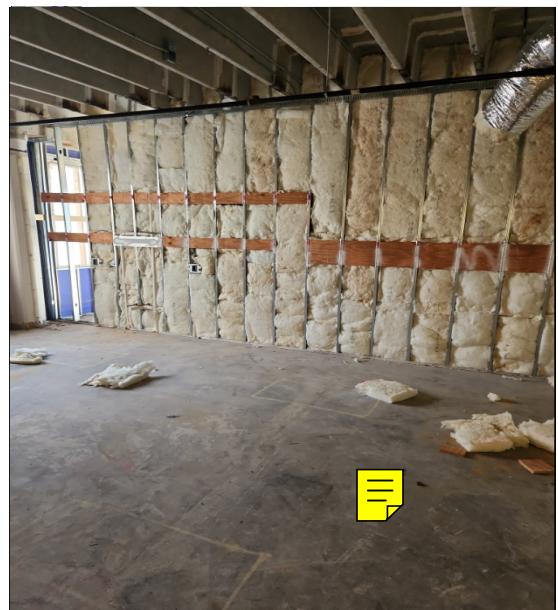

Continue in wall insulation and cover up in area 3



Continue prep for kitchen grease trap install

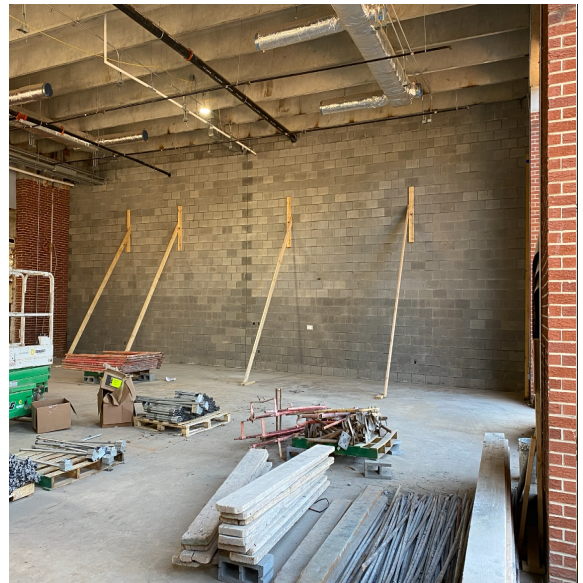

CMU wall at the cafeteria is complete



Completed exterior wall waterproofing in area 3



Site storm water system has been installed

NEXT WEEK – December 18 - December 22

- Install Kitchen grease traps
- Begin to install structural steel at the new security vestibule
- Complete all drywall cover up on the first and second floor in area 3
- Finish all CMU walls in area 2
- Begin painting CMU walls in the cafeteria and area 2

SCHEDULED DATE OF SUBSTANTIAL COMPLETION

- June 30, 2024

Final Completion

- June 30, 2024

PREPARED BY:

Jahaziel Lee, Carroll Daniel Construction Co.
