

An aerial photograph of Grady High School in Atlanta, Georgia. The image shows the school's main building complex on the left, a large stadium with tiered seating in the center, and a football field with yard lines and goalposts on the right. In the background, a dense line of trees separates the school grounds from the Atlanta city skyline, which is visible under a clear sky.

Weekly Construction Progress Report

Grady High School

Week Ending: 6/12/2020

PARRISH
CONSTRUCTION GROUP

Weekly Updates

THIS WEEK

- Parrish has continued to take measures to comply with the CDC and OSHA recommendations to keep the jobsite safe
- MEP rough-in above ceiling and on Roof
- Completed tear off and replacement of Theater Building Roof
- Continuing TPO Install on 8th Street Building
- Completed metal coping on 8th Street building and Theater.
- Installation of Water Source Heat Pumps complete
- Point and Patch 8th Street classroom walls.
- Installation of steel reinforcements in Theater Building
- Masonry Restoration ongoing at C Allen Building
- Setting Steel in basement of new addition
- Installing remaining storm piping
- Installing Toilet Fixtures in 8th Street Building

NEXT WEEK – 6.15.2020 – 6.19.2020

- Continue MEP rough-in above ceiling and on Roof
- Installing Toilet Partitions in 8th Street Group Bathrooms
- Continue rough in for HVAC Controls
- Continue TPO Roof install at 8th street and Theater buildings, starting Practice Gym Roof
- Begin Epoxy in 8th Street Single Bathrooms
- Continue Masonry Restoration & Waterproofing
- Begin underground electrical for new addition
- Painting 8th Street Building classrooms.
- Begin Grading Parking Lot
- Begin Demo in Performance Gym Lobby



Budget & Schedule

BUDGET

Construction Budget

- \$34,900,000.00

Budget Status

- \$ 3,808,514.49

SCHEDULE

Completion Date

- July 29,2021

Schedule Status

- On Schedule



ADDITIONAL INFO

- Scheduled Substantial Completion Date
 - July 29, 2021
- Completed By
 - Will Henry, PCG
- Copies To
 - Danny Gutlay, APS
 - Sandra Horton, APS
 - Katy Daugharty, CC
 - Bob Just, CC
 - John Rood, PCG
 - Darrell Bailey, PCG
 - Alex Johnson, PCG
 - Will Henry, PCG
 - Art Cofelice, PCG



Photo Updates

Roofing Progress at Existing Buildings



New Plumbing Fixtures and epoxy installed
in Group Restrooms in 8th Street



Photo Updates

Steel being set in basement of new addition



Plumbing Underground Complete



Photo Updates

Framing Family Living Center Chase Wall



MEP Rough-in in Family Living Center



Photo Updates

Point and Patch 8th Street Classrooms




Installing HVAC Curbs on 8th Street building



Photo Updates

Roofing on Theater Building

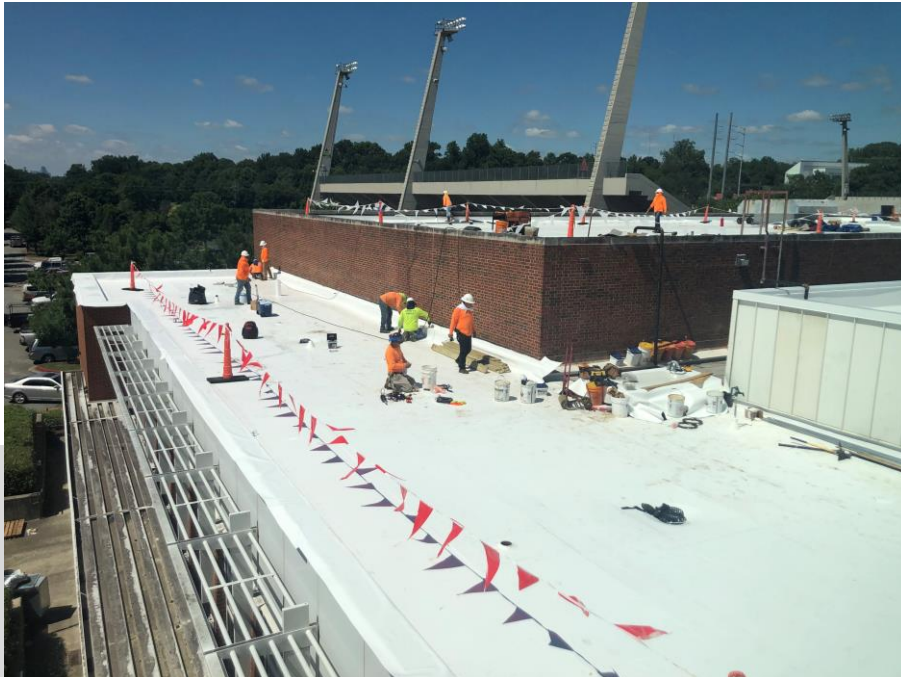

Painting 8th Street Classrooms

