

An aerial photograph of Midtown High School. The school building is a large, multi-story structure with a flat roof, situated on the left side of the image. To its right is a large, open field with white yard lines, likely a football or soccer field. In the background, a dense line of trees separates the school from a city skyline, which includes several tall skyscrapers. The sky is clear and blue.

Weekly Construction Progress Report

Midtown High School
Week Ending: 1/8/2021

PARRISH
CONSTRUCTION GROUP

Weekly Updates

THIS WEEK

- MEP overhead on second floor of new addition.
- MEP overhead on third floor of new addition.
- MEP overhead on fourth floor of new addition.
- Continue fire sprinkler third floor and Stair 1 Riser.
- Plumbing Rough-in fourth floor.
- Continued exterior metal framing and sheathing.
- Granite installation at West elevation
- Hang, Tape, and finish gypsum board
- Firestopping Second, and Third Floor of New Addition.
- Waterproofing applied on North, and West side of new addition.
- Complete plywood framing at high roof overhang for metal panels.
- Continue brick red brick install at south elevation and black brick at east elevations.
- Close in window opening with temporary plastic to dry in building temporarily.

NEXT WEEK – 1.11.2021 – 1.15.2021

- Continue MEP overhead and rough-in on Second, Third, and Fourth floors of the new addition.
- Continue brick red brick install at south elevation and black brick at east elevations.
- Continue waterproofing exterior at new addition.
- Continue interior and exterior metal framing.
- Continue exterior sheathing and waterproofing at new addition.
- Continue firestopping second and third floor of new addition.
- Continue granite installation at west elevation.
- Begin fire sprinkler install on 4th floor of new addition.
- Fireproofing at new addition bridge.
- Close in window opening with temporary plastic to dry in building temporarily.



Budget & Schedule

BUDGET

Construction Budget

- \$34,900,000.00

Budget Status

- \$ 21,611,125.84

SCHEDULE

Completion Date

- July 29,2021

Schedule Status

- On Schedule



ADDITIONAL INFO

- Scheduled Substantial Completion Date
 - July 29, 2021
- Completed By
 - Will Henry, PCG
- Copies To
 - Danny Gutlay, APS
 - Sandra Horton, APS
 - Katy Daugharty, CC
 - Bob Just, CC
 - Jim Fallon, PCG
 - Darrell Bailey, PCG
 - Alex Johnson, PCG
 - Will Henry, PCG
 - Art Cofelice, PCG
 - Travis Disbro, PCG



Photo Updates

New Addition Progress – North Elevation



Black Brick Progress at New Addition Patio



Photo Updates

Granite Progress on West Elevation at New Addition



MEP Overhead Progress 4th Floor of New Addition



Photo Updates

South Elevation Brick Progress at New Addition




Fire Sprinkler Progress in Stair 1 of New Addition



Photo Updates

Low Voltage Installation Progress at New Addition

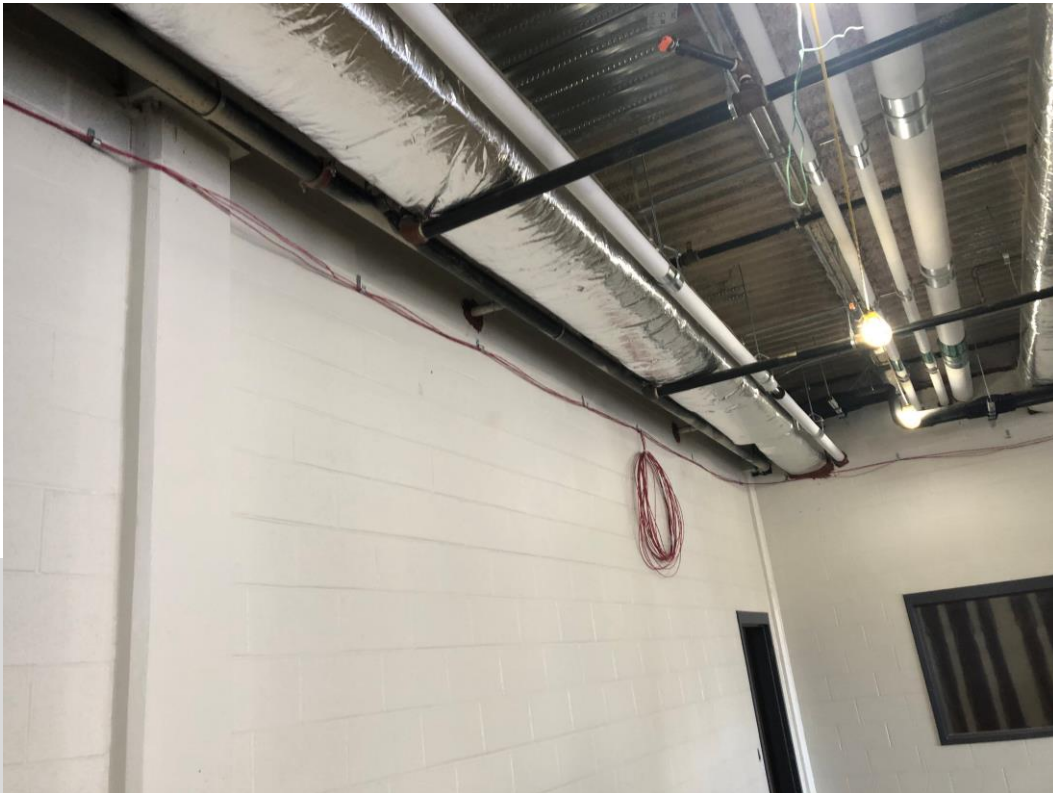

Plumbing Rough-In 4th Floor Progress of New Addition

