

An aerial photograph of Midtown High School. The school building is a large, multi-story structure with a flat roof, situated on the left side of the image. To the right of the building is a large, open field, likely a soccer field, with a goal visible. In the background, a dense line of trees separates the school from a city skyline, which includes several tall skyscrapers. The sky is clear and blue.

Weekly Construction Progress Report

Midtown High School
Week Ending: 2/19/2021

PARRISH
CONSTRUCTION GROUP

Weekly Updates

THIS WEEK

- MEP overhead on second, third and fourth floor of new addition.
- Continue fire sprinkler fourth floor and Stair Riser.
- Firestopping Fourth Floor of New Addition.
- Grading East elevation in preparation for Hardscapes.
- Begin Digging foundations for switchback ramp on East Elevation.
- Continue brick install at North elevations.
- Continue Brick Installation at Patio Roof.
- Install cast stone windowsills and Parapet Caps.
- Cleaning of Brick at South Elevation.
- Continue Installing Windows at South Elevation.
- Continue installing Curtainwall at East Elevation.
- Continue fire sprinkler install on 4th floor of new addition.

NEXT WEEK – 2.22.2021 – 2.26.2021

- Continue MEP overhead and rough-in on Second, Third, and Fourth floors of the new addition.
- Setting HVAC units on New Addition Building (Pending weather).
- Complete red brick install at South elevations.
- Continue Red brick install at North and West Elevations.
- Continue interior metal framing.
- Continue firestopping fourth floor of new addition.
- Acoustical Ceiling Grid install Second Floor of New Addition.
- Complete installing curtainwall frames on East Elevation.
- Installing light and Low-Voltage fixtures.
- Installing Windows at South Elevation of New Addition.
- Continue preparing for hardscapes on East Elevation.
- Pour Concrete Foundations at East Elevation Hardscapes.
- Hanging Gypsum Board in Media Center.



Budget & Schedule

BUDGET

Construction Budget

- \$34,900,000.00

Budget Status

- \$ 24,746,340.44

SCHEDULE

Completion Date

- July 29,2021

Schedule Status

- On Schedule



ADDITIONAL INFO

- Scheduled Substantial Completion Date
 - July 29, 2021
- Completed By
 - Will Henry, PCG
- Copies To
 - Danny Gutlay, APS
 - Sandra Horton, APS
 - Katy Daugharty, CC
 - Bob Just, CC
 - Jim Fallon, PCG
 - Alex Johnson, PCG
 - Will Henry, PCG
 - Art Cofelice, PCG
 - Travis Disbro, PCG
 - Tyler Cobb, PCG
 - Paul Cobb, PCG



Photo Updates

New Addition East Elevation Grading For Hardscapes




New Addition Progress – North Elevation



Photo Updates

Stuffing Insulation in Media Center Metal Stud Walls

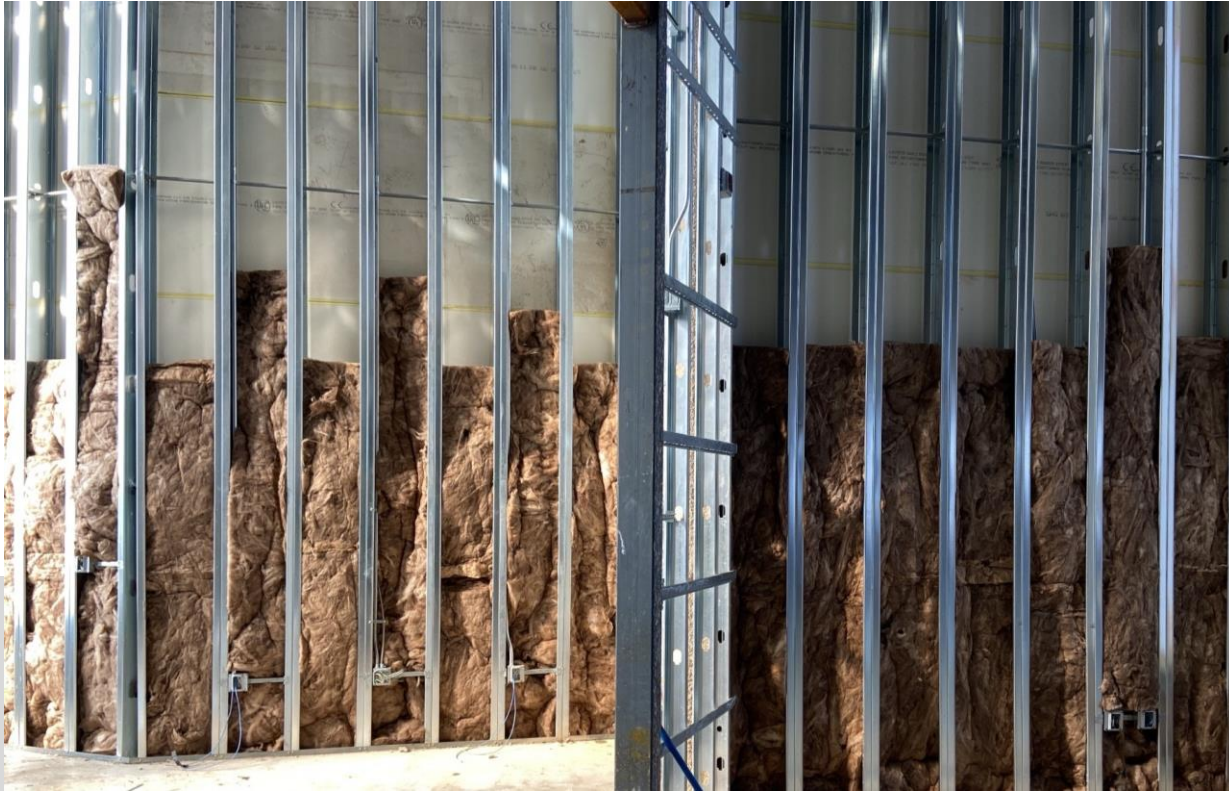

Media Center Ceiling Framing Progress



Photo Updates

South Elevation Window Progress



South Elevation Window Progress

