



Weekly Construction Progress Report

**Midtown High School
Week Ending: 3/5/2021**

PARRISH
CONSTRUCTION GROUP

Weekly Updates

THIS WEEK

- MEP overhead on second, third and fourth floor of new addition.
- Firestopping Fourth Floor of New Addition.
- Poured Concrete Walls for switchback ramp on East Elevation.
- Continue brick install at West elevations.
- Set HVAC units on New Addition Building.
- Install cast stone Parapet Caps at Patio Roof.
- Cleaning of Brick at South and North Elevation.
- Completed Installing windows at South Elevation.
- Completed Storefront frame installation at South Elevation of New Addition.
- Begin Storefront Installation at North Elevation of New Addition.
- Continue fire sprinkler install on 4th floor of new addition.
- Begin Metal Panel Installation at South West Elevation.

NEXT WEEK – 3.08.2021 – 3.12.2021

- Continue MEP overhead and rough-in on Second, Third, and Fourth floors of the new addition.
- Complete Red brick install at West Elevations.
- Continue interior metal framing and Gypsum Board Install.
- Continue firestopping fourth floor of new addition.
- Acoustical Ceiling Grid install Second Floor of New Addition.
- Installing light and Low-Voltage fixtures.
- Installing Storefront frames at North Elevation of New Addition.
- Pour Concrete Stairs at East Elevation Hardscapes.
- Continue Metal Panel Installation at South Elevation.
- Begin Elevator Installation.



Budget & Schedule

BUDGET

Construction Budget

- \$34,900,000.00

Budget Status

- \$ 26,463,871.02

SCHEDULE

Completion Date

- July 29,2021

Schedule Status

- On Schedule




ADDITIONAL INFO

- Scheduled Substantial Completion Date
 - July 29, 2021
- Completed By
 - Will Henry, PCG
- Copies To
 - Danny Gutlay, APS
 - Sandra Horton, APS
 - Katy Daugharty, CC
 - Bob Just, CC
 - Jim Fallon, PCG
 - Alex Johnson, PCG
 - Will Henry, PCG
 - Art Cofelice, PCG
 - Travis Disbro, PCG
 - Tyler Cobb, PCG
 - Paul Cobb, PCG



Photo Updates

New Addition Progress – East Elevation

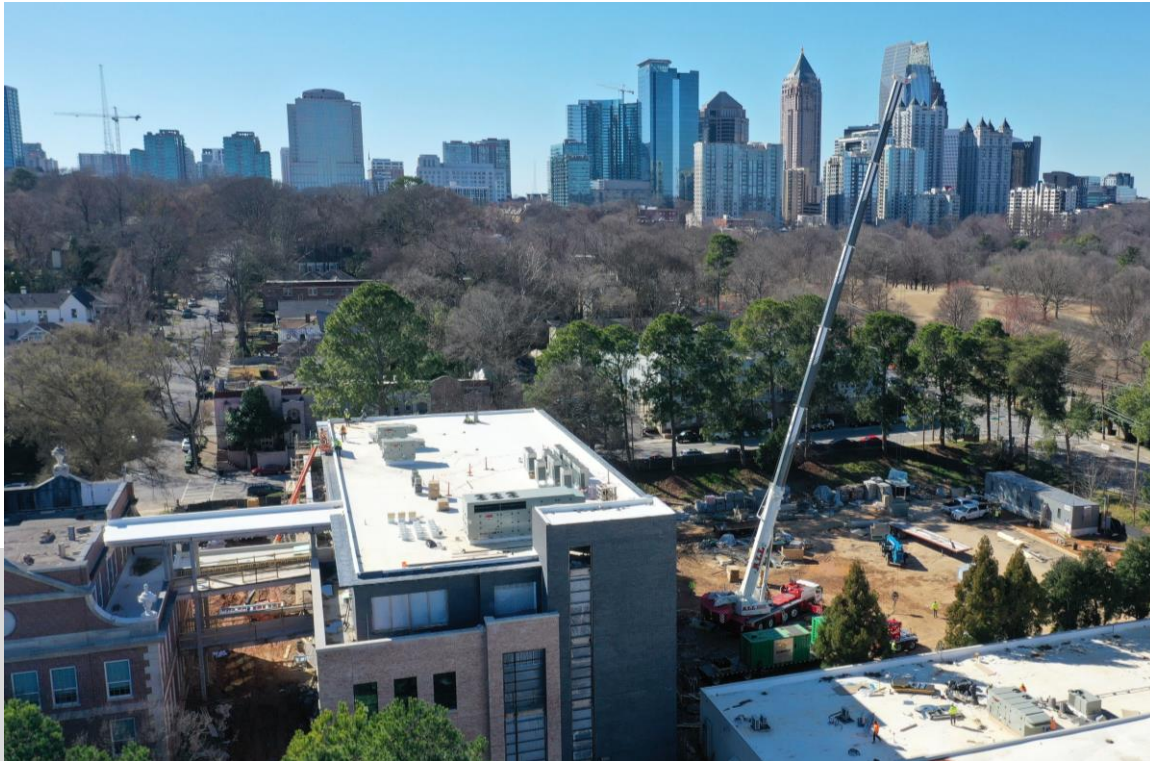

New Addition Progress – North Elevation



Photo Updates

Setting HVAC Units on New Addition Roof



Setting HVAC Units on New Addition Roof



Photo Updates

HVAC Units Set on New Addition Rooftop



ACM Metal Panel Progress at South West Elevation



Photo Update

Completed Installation of Gypsum Board on Media Center Metal Stud Walls




Storefront Frames Installed at North Elevation



Photo Updates

Storefront Frames Installed at South Elevation

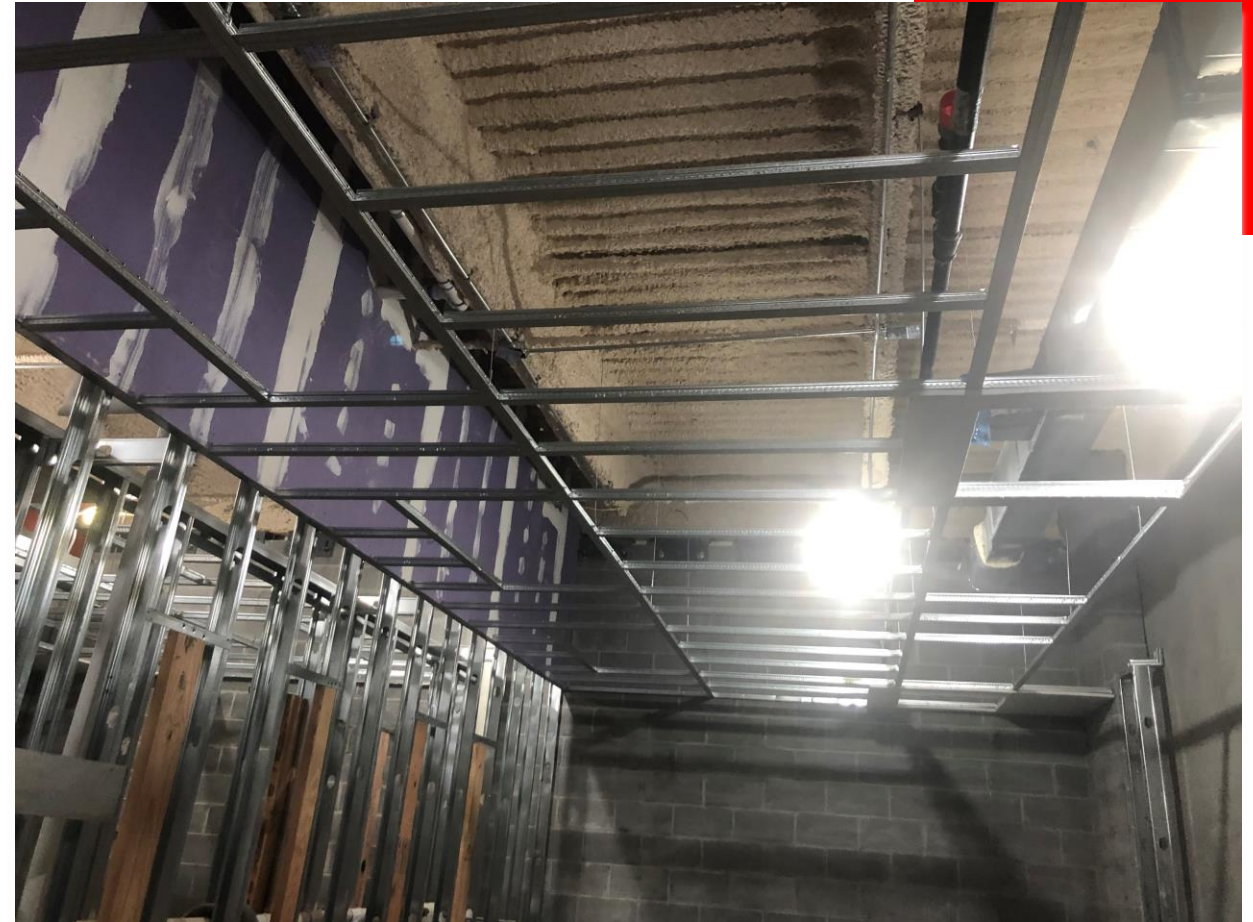

Metal Framing Progress in 4th Floor Bathroom

