



Weekly Construction Progress Report

Grady High School

Week Ending: 5/15/2020

PARRISH
CONSTRUCTION GROUP

Weekly Updates

THIS WEEK

- Parrish has continued to take measures to comply with the CDC and OSHA recommendations to keep the jobsite safe
- Completed Underground Detention System
- Completed concrete foundations for new addition
- Poured South Wall of new addition building
- Finished installing scaffolding for Masonry Restoration at Charles Allen Building
- MEP rough-in above ceiling and on Roof
- Begin Tear off and replacement of Theater Building Roof
- Continuing TPO Install on 8th Street Building
- Poured elevator pit
- Continued to install flashing and weep holes at theater wall
- Prepped 8th street group bathrooms for Epoxy
- Started Foundation Block

NEXT WEEK – 5.18.2020 – 5.22.2020

- Begin underground plumbing at new addition
- MEP rough-in above ceiling and on Roof
- Remove existing HVAC units that are to be replaced
- Continue TPO Roof install at 8th street and Theater buildings
- Begin Epoxy in 8th Street Bathrooms
- Begin Masonry Restoration
- Demo ACT ceilings in classrooms in 8th Street
- Install storm and sewer lines for new addition
- Jack and Bore into manhole on 10th Street
- Waterproofing wall and installing foundation drainage system



Budget & Schedule

BUDGET

Construction Budget

- \$34,900,000.00

Budget Status

- \$ 1,416,729.77

SCHEDULE

Completion Date

- July 29,2021

Schedule Status

- On Schedule



ADDITIONAL INFO

- Scheduled Substantial Completion Date
 - July 29, 2021
- Completed By
 - Will Henry
- Copies To
 - Danny Gutlay, APS
 - Sandra Horton, APS
 - Katy Daugharty, CC
 - John Rood, PCG
 - Darrell Bailey, PCG
 - Alex Johnson, PCG
 - Will Henry, PCG
 - Art Cofelice, PCG



Photo Updates

Jobsite Overview



Pouring Concrete at South Wall of New Addition



Photo Updates

South Wall of New Addition



Pouring Elevator Pit for New Addition



Photo Updates


Prepping parking lot for New Addition



Installation of foundation block

Photo Updates

Roofing on 8th Street Building Progress

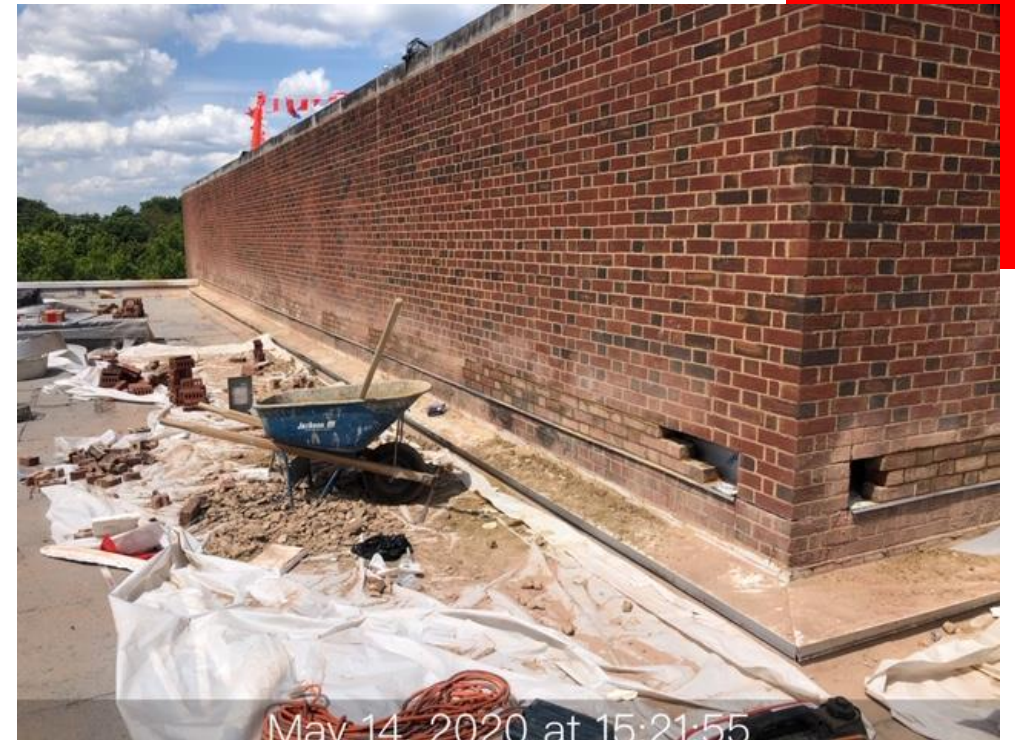

Flashing on Theater Walls being installed

Photo Updates

Stage Floor Demo Complete



Installation of TPO Roof on Theater Building

