

An aerial photograph of Midtown High School. The school building is a large, multi-story structure with a flat roof, situated on the left side of the image. To the right of the building is a large, open field, likely a soccer field, with a goal visible. In the background, a dense line of trees separates the school from a city skyline, which includes several tall skyscrapers. The sky is clear and blue.

# **Weekly Construction Progress Report**

**Midtown High School**  
**Week Ending: 5/21/2021**

**PARRISH**  
CONSTRUCTION GROUP

# Weekly Updates

## THIS WEEK

- MEP startup and trim out in new addition building.
- Continue Metal Panel Installation at New Addition.
- Continue Patio Roofing system.
- Continue hardscapes on the South Elevations.
- Complete VCT and flooring finishes in New Addition Building.
- Completed Installing Toilet Partitions and Accessories.
- Continue Multipurpose and CTAE build back in 8<sup>th</sup> street building.
- Continued Curtainwall Installation at New Addition and C. Allen Building Bridge.
- Continue Terrazzo Flooring in Charles Allen building Administration Area.
- Completed Canopy Install on East Elevation.
- Complete installing glass at New Addition Bridge Curtainwall.
- Pour Foundations and begin installing Granite Walls on South Elevation.

## NEXT WEEK – 5.24.2021 – 5.28.2021

- Complete MEP Startup and trim out in the New Addition Building.
- Continue hardscapes on the South Elevations.
- Complete Patio Roofing system.
- Continue Metal Panel Installation.
- Complete Remaining Flooring Finishes in new Addition Building.
- Continue Curtainwall Installation at New Addition and C. Allen Building Bridge.
- Complete Trim at New Addition Bridge Curtainwall.
- New Addition Parking topcoat.
- Complete 8<sup>th</sup> Street Multipurpose and CTAE Build back in 8<sup>th</sup> Street.
- Final Cleaning in New Addition Building.



# Budget & Schedule

## BUDGET

Construction Budget

- \$34,900,000.00

Budget Status

- \$ 29,378,364.35

## SCHEDULE

Completion Date

- July 29,2021

Schedule Status

- On Schedule



## ADDITIONAL INFO

- Scheduled Substantial Completion Date
  - July 29, 2021
- Completed By
  - Will Henry, PCG
- Copies To
  - Danny Gutlay, APS
  - Sandra Horton, APS
  - Katy Daugharty, CC
  - Bob Just, CC
  - Jim Fallon, PCG
  - Alex Johnson, PCG
  - Will Henry, PCG
  - Art Cofelice, PCG
  - Travis Disbro, PCG
  - Tyler Cobb, PCG
  - Paul Cobb, PCG





# Photo Updates

Carpet Installation Completed in All Offices in the New Addition Building



East Elevation Canopy Installed at the  
New Addition Building



# Photo Updates

Curtainwall and Bridge Progress at  
South Elevation



New Addition Building Elevator Completed





# Photo Updates

## VCT Completed in New Addition Building




## Toilet Partitions Completed in New Addition Building Restrooms



# Photo Updates

Patio Roof Paver Progress

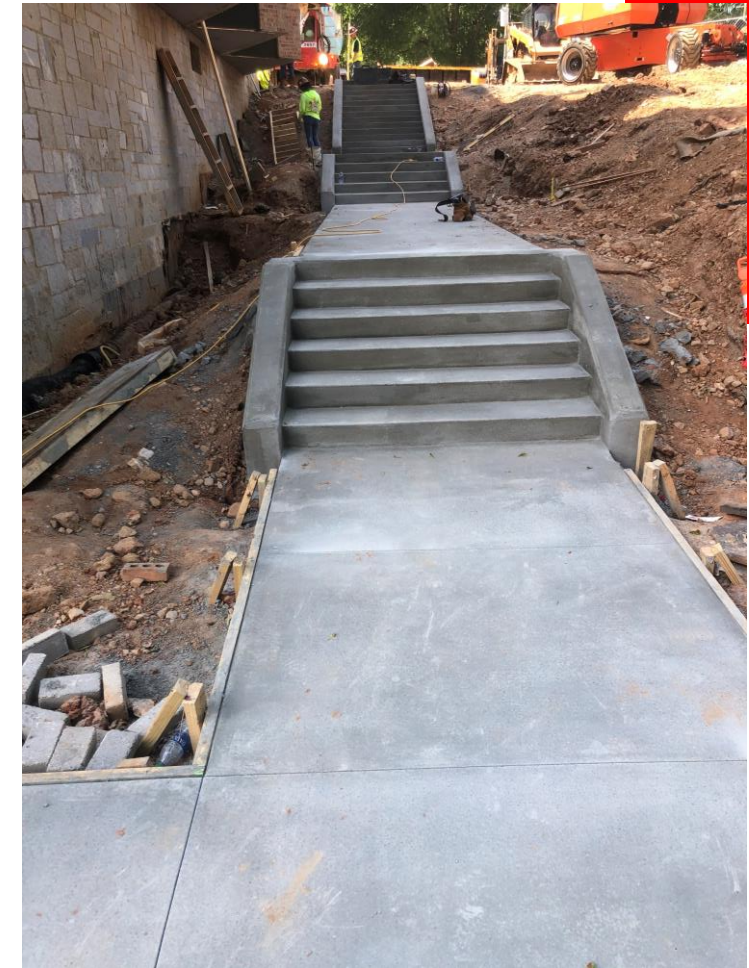

West Elevation Hardscapes Completed

