

An aerial photograph of Midtown High School campus. The school buildings are on the left, featuring flat roofs and brickwork. To the right is a large sports field with yard lines and a goalpost. In the background, a dense forest separates the school from a city skyline with various skyscrapers under a clear sky.

Weekly Construction Progress Report

Midtown High School
Week Ending: 6/04/2021

PARRISH
CONSTRUCTION GROUP

Weekly Updates

THIS WEEK

- Continue Metal Panel Installation at New Addition.
- Complete Patio Roofing system.
- Continue hardscapes on the South Elevations.
- Completed Installing Toilet Partitions and Accessories.
- Complete Multipurpose and CTAE build back in 8th street building.
- Continued Curtainwall Installation at New Addition and C. Allen Building Bridge.
- Completed Terrazzo Flooring in Charles Allen building Administration Area & Started Bridge Terrazzo Prep.
- Final Cleaning in New Addition Building.
- Demolition and Reinstall of HVAC in Charles Allen Building.
- Demolition in Charles Allen Building, and 8th Street Ground floor.
- Pour 4th Floor Bridge Connector Slab into Charles Allen Building.
- Removing Portable Classrooms from front Campus.

NEXT WEEK – 6.07.2021 – 6.11.2021

- Continue hardscapes on the South Elevations.
- Continue Metal Panel Installation at Bridge.
- Complete Remaining Flooring Finishes in new Addition Building.
- Continue Curtainwall Installation at New Addition and C. Allen Building Bridge.
- Complete Trim out at New Addition Bridge Curtainwall.
- Final Cleaning in New Addition Building.
- Demolition in Charles Allen Building, and 8th Street Ground floor.
- Continue swap out of HVAC units in Charles Allen Building.
- Removing Portable Classrooms from front Campus.
- Staging roofing material on Charles Allen Roof, following Portable classroom removal.



Budget & Schedule

BUDGET

Construction Budget

- \$34,900,000.00

Budget Status

- \$ 30,677,596.39

SCHEDULE

Completion Date

- July 29,2021

Schedule Status

- On Schedule



ADDITIONAL INFO

- Scheduled Substantial Completion Date
 - July 29, 2021
- Completed By
 - Will Henry, PCG
- Copies To
 - Danny Gutlay, APS
 - Sandra Horton, APS
 - Katy Daugharty, CC
 - Bob Just, CC
 - Jim Fallon, PCG
 - Alex Johnson, PCG
 - Will Henry, PCG
 - Art Cofelice, PCG
 - Travis Disbro, PCG
 - Tyler Cobb, PCG
 - Paul Cobb, PCG



Photo Updates

New Addition Building
Patio Pavers Completed



New Addition Building Media Center



Photo Updates

Trophy Case Installed at New Addition




Striping, Signage, and Parking Lot Lighting Completed at New Addition Building



Photo Updates

Charles Allen Ceiling and HVAC Demo Progress

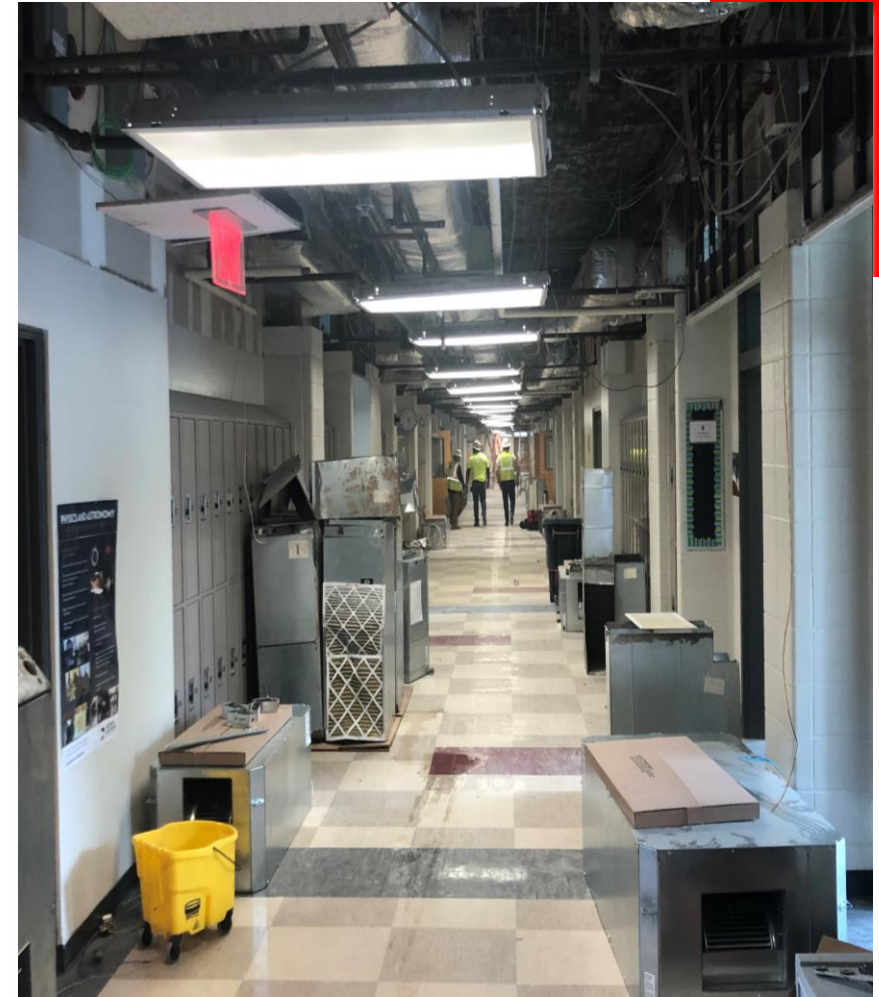


Charles Allen Building HVAC and Ceiling Demo Progress



Photo Updates

Water Source Heat Pump Swap Completed
4th Floor of Charles Allen Building

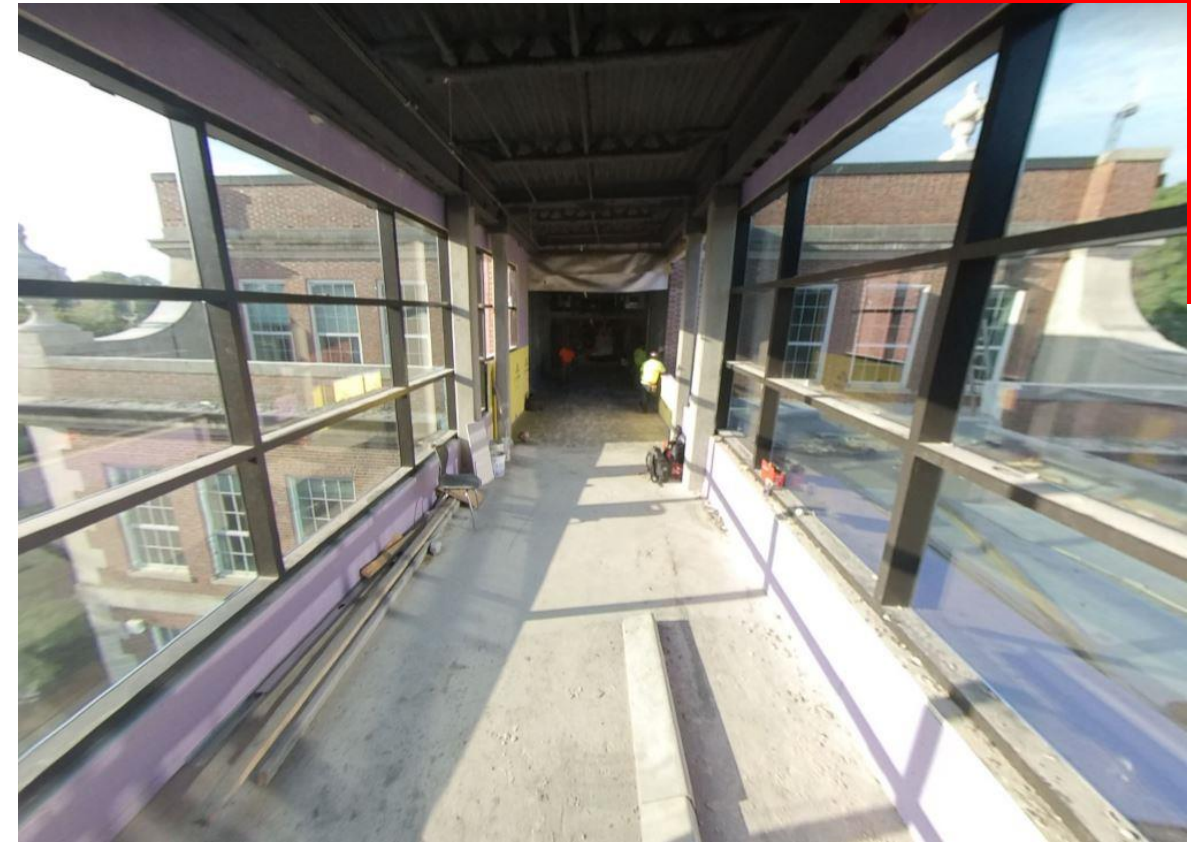

4th Floor New Addition to Charles Allen
Bridge Progress

