

An aerial photograph of Midtown High School. The school building is a large, multi-story structure with a flat roof, situated on the left side of the image. To the right of the building is a large, open field, likely a soccer field, with a goal visible. In the background, a dense line of trees separates the school from a city skyline, which includes several tall skyscrapers. The sky is clear and blue.

Weekly Construction Progress Report

Midtown High School

Week Ending: 6/11/2021

PARRISH
CONSTRUCTION GROUP

Weekly Updates

THIS WEEK

- Continue hardscapes on the South Elevations.
- Complete Curtainwall Installation at New Addition and C. Allen Building Bridge.
- Complete Terrazzo Flooring at New Addition-Charles Allen Bridge.
- Final Cleaning in New Addition Building.
- Demolition and Reinstall of HVAC in Charles Allen Building.
- Demolition in Charles Allen Building, and 8th Street Ground floor and Charles Allen Building Rooftop Units.
- Removed Portable Classrooms from front Campus.
- Staging roofing material on Charles Allen Roof, following Portable classroom removal.
- Performance and Practice Gym Court Sanding and Refinishing.
- Complete Remaining Flooring Finishes in new Addition Building.

NEXT WEEK – 6.14.2021 – 6.18.2021

- Hardscapes on the South Elevations.
- Complete Metal Panel Installation at Bridge.
- Complete Trim out at New Addition Bridge Curtainwall.
- Final Cleaning in New Addition Building.
- Continue swap out of HVAC units in Charles Allen Building.
- Begin Landscaping and Front Campus Porous Paver Grading.
- Performance and Practice Gym Court Sanding and Refinishing.
- Roofing Charles Allen Building Roof
- Setting New HVAC units on Charles Allen Building Roof.
- Begin Epoxy Flooring in Charles Allen Building.



Budget & Schedule

BUDGET

Construction Budget

- \$34,900,000.00

Budget Status

- \$ 30,677,596.39

SCHEDULE

Completion Date

- July 29,2021

Schedule Status

- On Schedule



ADDITIONAL INFO

- Scheduled Substantial Completion Date
 - July 29, 2021
- Completed By
 - Will Henry, PCG
- Copies To
 - Danny Gutlay, APS
 - Sandra Horton, APS
 - Katy Daugharty, CC
 - Bob Just, CC
 - Jim Fallon, PCG
 - Will Henry, PCG
 - Art Cofelice, PCG
 - Travis Disbro, PCG
 - Tyler Cobb, PCG
 - Paul Cobb, PCG



Photo Updates

New Addition Building
Northwest Elevation



Charles Allen Building – New Classroom
Addition Building Overview



Photo Updates

Front Campus of Charles Allen Demo
Progress – Mobile Classrooms Removed



Charles Allen Building Rooftop Units
Removed



Photo Updates

Performance Gym Court Refinishing
with Midtown Knights Logo




Performance Gym Mechanical
Room#2 HVAC Demo Progress



Photo Updates

Water Source Heat Pump Swap Completed 3rd Floor of Charles Allen Building

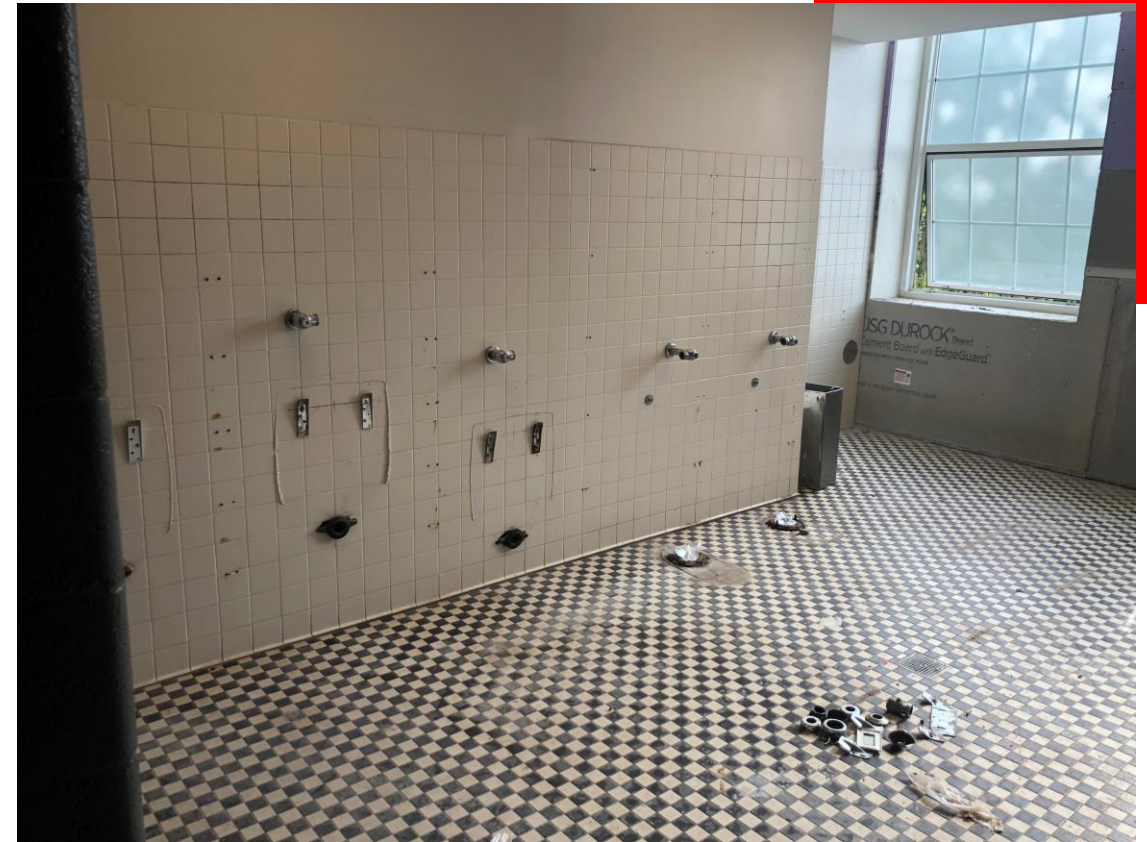

Charles Allen Building Group Restrooms Demo Progress



Photo Updates



New Classroom Addition Building East Elevation

