



Weekly Construction Progress Report

Grady High School

Week Ending: 7/3/2020

PARRISH
CONSTRUCTION GROUP

Weekly Updates

THIS WEEK

- Continue MEP rough-in above ceiling and on Roof.
- Continue rough in for HVAC Controls.
- Continue TPO Roof install at Practice & Performance Gym Roof.
- Begin Flooring Install.
- Continue Masonry Restoration & Waterproofing.
- Pour First floor Slab at New Addition.
- Painting 8th Street Building classrooms.
- Demo Performance Gym Masonry Walls and Finishes.
- Begin Ceiling Grid install in 8th Street Classrooms.
- Complete Painting in 8th Street Building.
- Begin Lighting reinstallation.

NEXT WEEK – 7.06.2020 – 7.10.2020

- Begin erecting steel for the new addition.
- Continue rough in for HVAC Controls.
- Continue lighting installation.
- Continue low voltage installation in 8th St. building.
- Begin installing ceiling grid in 8th St. building.
- Begin grading and placing stone for new parking lot.
- Continue TPO Roof install at 8th street and Practice Gym Roof.
- Setting HVAC rooftop units on 8th Street, Theater, & Practice Gym buildings.



Budget & Schedule

BUDGET

Construction Budget

- \$34,900,000.00

Budget Status

- \$ 7,910,164.78

SCHEDULE

Completion Date

- July 29,2021

Schedule Status

- On Schedule



ADDITIONAL INFO

- Scheduled Substantial Completion Date
 - July 29, 2021
- Completed By
 - Alex Johnson, PCG
- Copies To
 - Danny Gutlay, APS
 - Sandra Horton, APS
 - Katy Daugharty, CC
 - Bob Just, CC
 - John Rood, PCG
 - Darrell Bailey, PCG
 - Alex Johnson, PCG
 - Will Henry, PCG
 - Art Cofelice, PCG
 - Travis Disbro, PCG



Photo Updates

New Addition Slab Pour



New Addition Slab Pour



Photo Updates

New Addition Slab Pour




New Addition Slab Pour



Photo Updates

Family Living Center Drywall

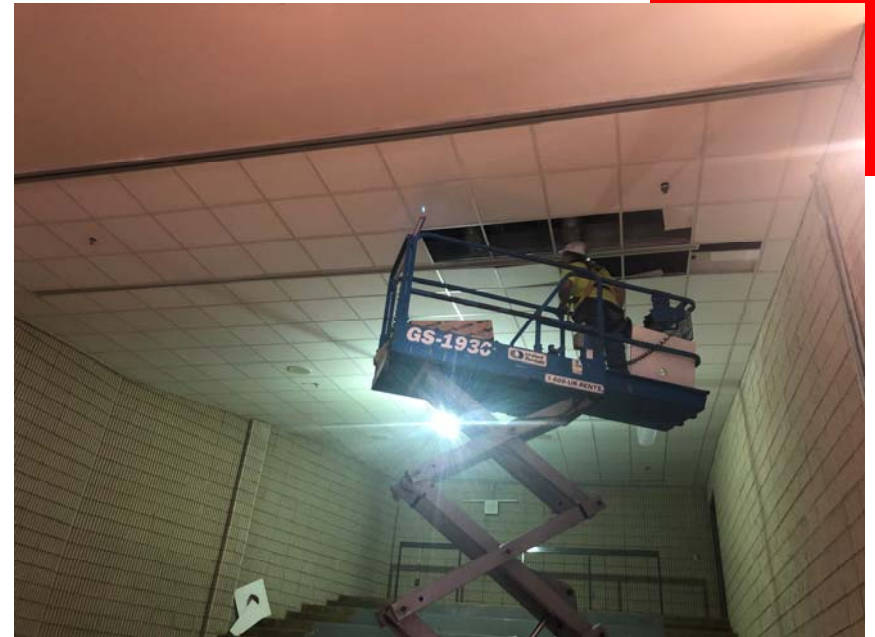

Ceiling Grid and Tiles in Theater



Photo Updates

New Addition Slab Pour



New Addition Slab Pour



Photo Updates

Installing Ceiling Grid in 8th St. Building



Bulkhead Framing for Performance Gym

