

An aerial photograph of Grady High School in Atlanta, Georgia. The image shows the school's main building, a large stadium with tiered seating, and a football field. In the background, the Atlanta skyline is visible under a clear sky. The image is in grayscale, except for a red vertical bar on the left edge.

Weekly Construction Progress Report

Grady High School

Week Ending: 7/24/2020

PARRISH
CONSTRUCTION GROUP

Weekly Updates

THIS WEEK

- Installed decking on second floor
- Continue MEP rough-in above ceiling and on Roof.
- MEP Trim out
- Drop Ceiling Tiles in Corridors
- Continue TPO Roof install at Practice & Performance Gym Roof.
- Installed Theater Seating
- Installed Carpet in Theater
- Continue Masonry Restoration & Waterproofing.
- Completed Performance Gym Masonry Walls and Finishes.
- Paved new addition Parking Lot
- Continue MEP Rough-in in Performance Gym.
- Completed steel erection on first floor of New Addition.
- Begin Third Floor perimeter steel erection.
- Lighting reinstallation in Theater Building.

NEXT WEEK – 7.27.2020 – 7.31.2020

- Continue trim out for MEP.
- Finish lighting installation throughout.
- Finish low voltage device installation.
- Erecting Third floor steel at new addition.
- Prepare second floor of new addition for slab pour.
- Complete unit startup.
- Continue TPO roof install at Performance Gym Roof.
- Continue installing metal coping.
- Finish painting Practice Gym.
- Complete stage floor in Theater.
- Final cleaning throughout.
- Performance Gym Epoxy Flooring



Budget & Schedule

BUDGET

Construction Budget

- \$34,900,000.00

Budget Status

- \$ 7,910,164.78

SCHEDULE

Completion Date

- July 29,2021

Schedule Status

- On Schedule



ADDITIONAL INFO

- Scheduled Substantial Completion Date
 - July 29, 2021
- Completed By
 - Will Henry, PCG
- Copies To
 - Danny Gutlay, APS
 - Sandra Horton, APS
 - Katy Daugharty, CC
 - Bob Just, CC
 - John Rood, PCG
 - Darrell Bailey, PCG
 - Alex Johnson, PCG
 - Will Henry, PCG
 - Art Cofelice, PCG
 - Travis Disbro, PCG



Photo Updates

Site Overview



New Addition Progress



Photo Updates

Progress at New Addition



Preparing New Addition
Parking Lot



Photo Updates

MEP Trim out and Cleaning complete in 8th
Street Classrooms




Group Bathroom Toilet Accessories
Installed



Photo Updates

Theater Ceiling complete

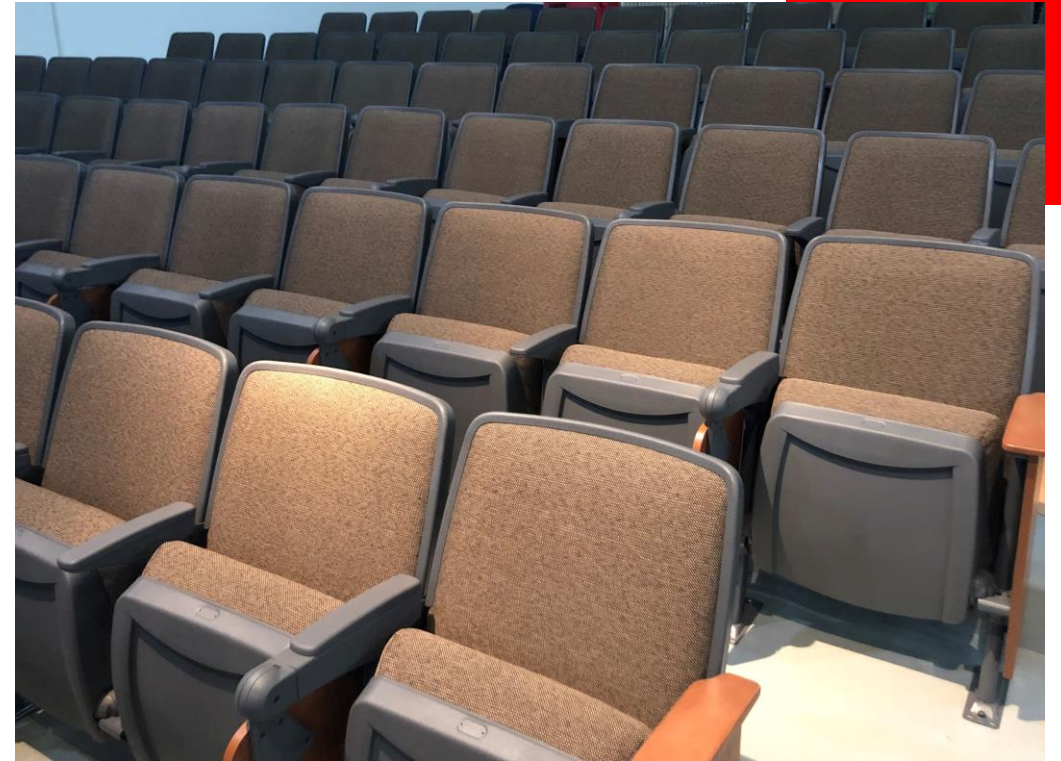


Theater Seats Installed



Photo Updates

Theater Carpet Installation Progress

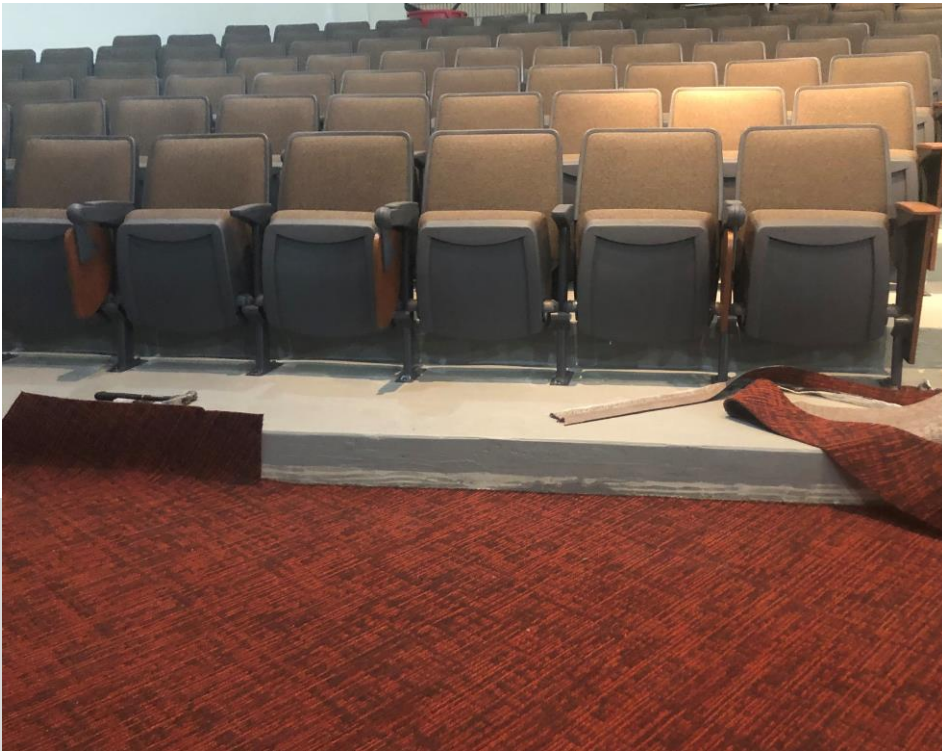

New CMU Wall progress in Performance Gym
