

An aerial photograph of Grady High School in Atlanta, Georgia. The image shows the school's main building, a large stadium with tiered seating, and a football field with yard lines. In the background, the Atlanta skyline is visible through a hazy atmosphere. The entire image is in grayscale, except for a solid red vertical bar on the far left edge.

Weekly Construction Progress Report

Grady High School

Week Ending: 08/28/2020

PARRISH
CONSTRUCTION GROUP

Weekly Updates

THIS WEEK

- Fireproofing perimeter of first floor at new addition.
- Completed metal coping at Performance Gym Roof.
- Finish epoxy flooring in performance gym.
- Poured second floor column wraps.
- Continue MEP overhead on ground floor of new addition.
- Began fourth floor metal decking.
- Completed steel sunshades at new addition.
- Continue CMU walls on ground floor of new addition.
- Completed storm structures and grading between Charles Allen and new addition.
- Third Floor Slab on Deck Prep
 - Third Floor concrete pour scheduled for Friday 8/28
- MEP overhead and rough-in in Performance Gym Lobby.
- Painted final coat of Performance Gym Lobby.

NEXT WEEK – 8.31.2020 – 9.04.2020

- Start exterior brick work on SE Corner of new addition.
- Continue CMU walls on ground floor of new addition.
- Continue MEP overhead and rough-in on First and Second floor of new addition.
- Continue Steel Erection for fourth floor.
- Complete installing lights and Mechanical Overhead work in Performance Gym Lobby
- Remove existing curtainwall system at Performance Gym Lobby and install the new curtainwall system.
- Begin forming third floor shear walls
- Begin forming column wraps
- Begin 2nd floor fireproofing



Budget & Schedule

BUDGET

Construction Budget

- \$34,900,000.00

Budget Status

- \$ 10,276,463.74

SCHEDULE

Completion Date

- July 29,2021

Schedule Status

- On Schedule



ADDITIONAL INFO

- Scheduled Substantial Completion Date
 - July 29, 2021
- Completed By
 - Will Henry, PCG
- Copies To
 - Danny Gutlay, APS
 - Sandra Horton, APS
 - Katy Daugharty, CC
 - Bob Just, CC
 - John Rood, PCG
 - Darrell Bailey, PCG
 - Alex Johnson, PCG
 - Will Henry, PCG
 - Art Cofelice, PCG
 - Travis Disbro, PCG



Photo Updates

New Addition Progress




New Addition Progress



Photo Updates

Fourth Floor Decking Progress

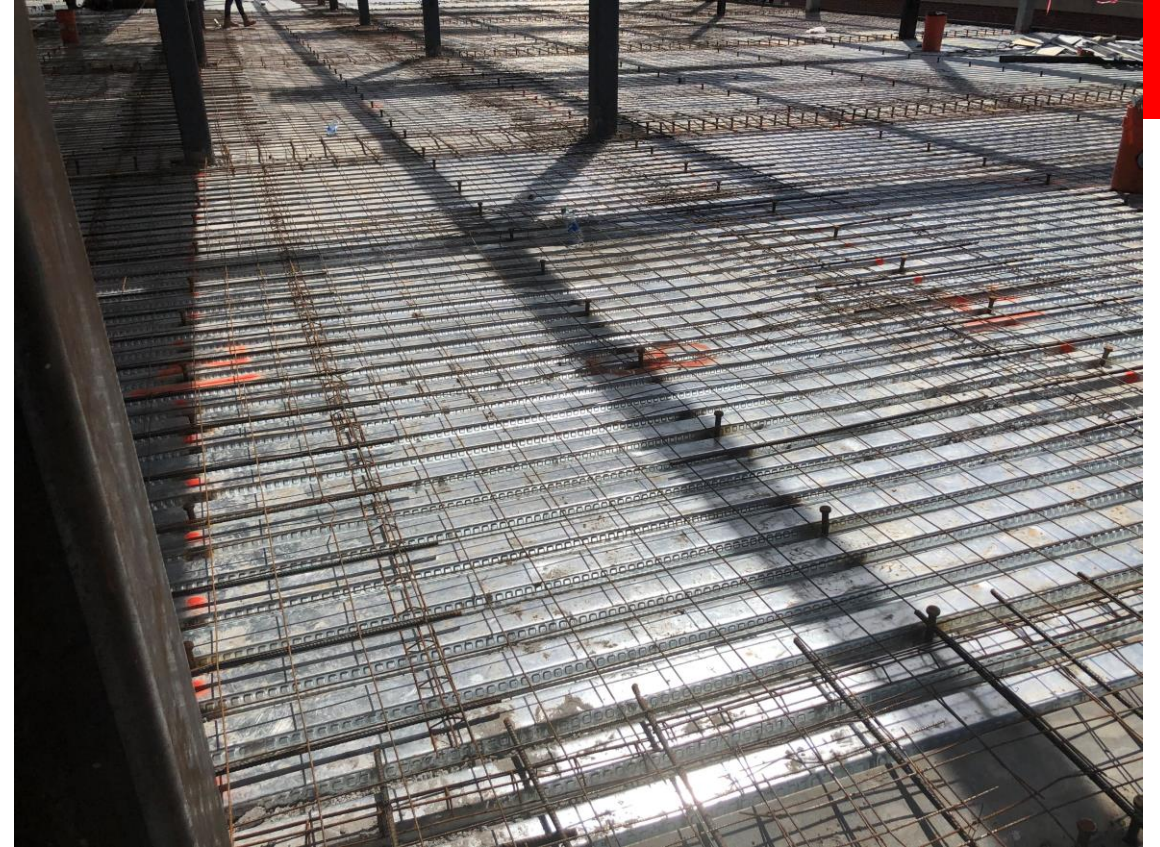

Third Floor Slab prepared for concrete pour



Photo Updates

Plumbing Roughed in at 2nd Floor Restroom



Second floor interior columns complete



Photo Updates

Interior CMU wall progress, Fireproofing, and MEP Overhead piping first floor



Exterior CMU and sheathing installed at west wall, ready for air/weather barrier



Photo Updates

Door and Hardware
installed in Performance
Gym Lobby



Ceramic Tile installed in
Performance Gym Lobby



Metal Coping installed at Performance
Gym Roof

