

An aerial photograph of Grady High School campus and stadium. The school buildings are on the left, and the large stadium with seating is in the center. A football field is visible in the foreground. In the background, a dense forest separates the campus from a city skyline with several tall skyscrapers under a clear sky.

# **Weekly Construction Progress Report**

**Grady High School**

**Week Ending: 11/13/2020**

**PARRISH**  
CONSTRUCTION GROUP

# Weekly Updates

## THIS WEEK

- MEP overhead on Second floor of new addition.
- MEP overhead on Third floor of new addition.
- Continue CMU install Third Floor of new addition.
- Continue Fire Sprinkler Third Floor.
- Steel Erection for Bridge Connection with Charles Allen Building.
- Pour Concrete Treads and Stair Landing at Stairwell 1 on East side of New Addition.
- Plumbing Rough-in third and fourth floor.
- Continued exterior metal framing.
- Complete TPO Roof system at high roof of new addition.
- Begin Spray Fireproofing Fourth Floor of New Addition.
- Interior Metal Framing 2<sup>nd</sup> Floor.
- Drywall Ceiling Framing 2<sup>nd</sup> Floor.
- Continue Brick Install at SE Corner.
- Firestopping First and Second Floor of New Addition.

## NEXT WEEK – 11.16.2020 – 11.20.2020

- Continue CMU walls on the third floor of the new addition.
- Continue MEP overhead and rough-in on First, Second, Third, and Fourth floors of the new addition.
- Continue brick Install SE Corner.
- Continue Waterproofing at New Addition.
- Continue interior and exterior metal framing.
- Continue Exterior Sheathing and Waterproofing at New Addition.
- Continue Firestopping First and Second Floor of New Addition.
- Granite Installation beginning at North East Elevation



# Budget & Schedule

## BUDGET

Construction Budget

- \$34,900,000.00

Budget Status

- \$ 17,406,598.10

## SCHEDULE

Completion Date

- July 29,2021

Schedule Status

- On Schedule



## ADDITIONAL INFO

- Scheduled Substantial Completion Date
  - July 29, 2021
- Completed By
  - Will Henry, PCG
- Copies To
  - Danny Gutlay, APS
  - Sandra Horton, APS
  - Katy Daugharty, CC
  - Bob Just, CC
  - Jim Fallon, PCG
  - Darrell Bailey, PCG
  - Alex Johnson, PCG
  - Will Henry, PCG
  - Art Cofelice, PCG
  - Travis Disbro, PCG





# Photo Updates

New Addition Progress



New Addition Progress





# Photo Updates

Interior Metal Framing at Media Center at New Addition



Interior Metal Framing at Media Center at New Addition






# Photo Updates



Stairwell 1 Completed at New Addition

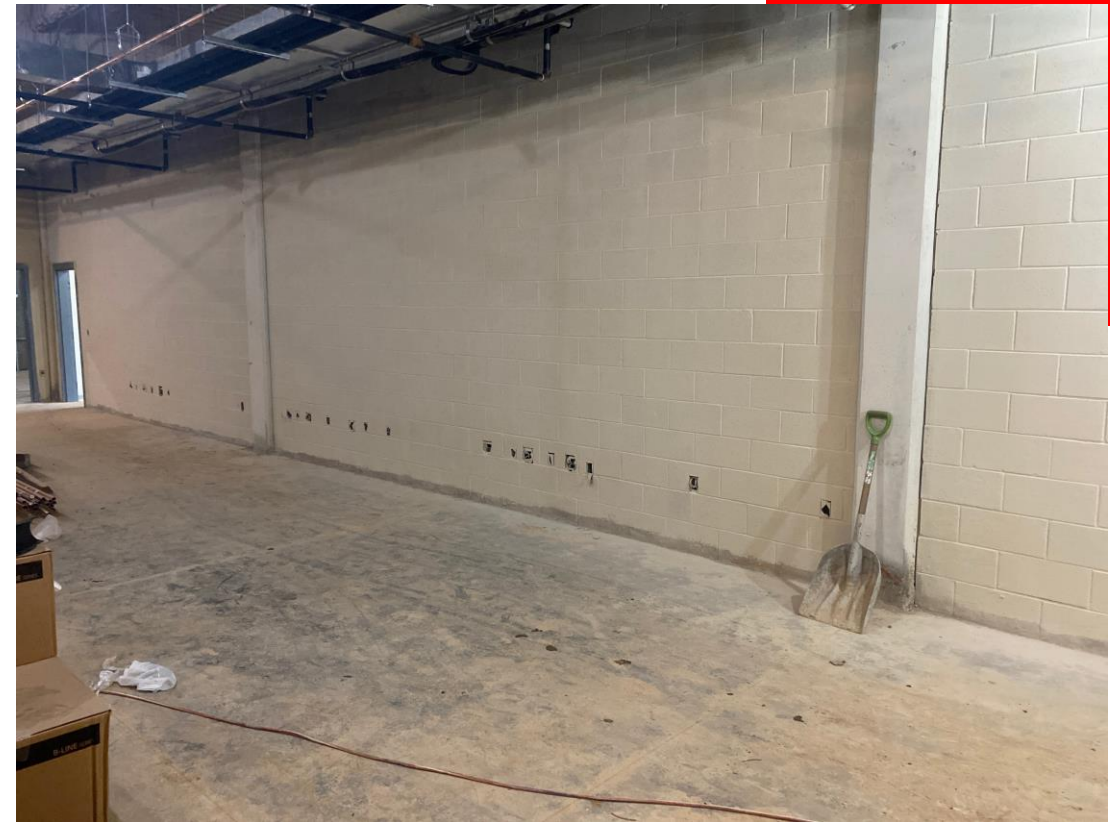

Blockfill installed at First Floor of New Addition





# Photo Updates

Red Brick Progress at South East Corner



Black Brick Progress at North East Corner





# Photo Updates

Bridge Decking at New Addition Bridge



Brick Progress at South Side of New Addition

