

An aerial photograph of Midtown High School. The school building is a large, multi-story structure with a flat roof, situated on the left side of the image. To the right of the building is a large, open field, likely a soccer field, with a goal visible. In the background, a dense line of trees separates the school from a city skyline, which includes several tall skyscrapers. The sky is clear and blue.

# **Weekly Construction Progress Report**

**Midtown High School**  
**Week Ending: 4/16/2021**

**PARRISH**  
CONSTRUCTION GROUP

# Weekly Updates

## THIS WEEK

- MEP overhead and trim out in new addition building.
- Completed Ceramic Tile Installation in Restrooms.
- Continue fire sprinkler on 4<sup>th</sup> floor of new addition.
- Continue Metal Panel Installation at North Elevation.
- Gypsum Board Finishing.
- Painting in Performance Gym.
- Continue Patio Roofing system.
- Continue hardscapes on the East and South East Elevations.
- Continue Epoxy flooring in New Addition Restrooms.
- Begin VCT and flooring finishes in New Addition Building.
- Begin Terrazzo Installation on Second Floor of New Addition Building.
- Completed Demolition and began build back in Old Media Center in 8<sup>th</sup> street building.
- Completed Curtainwall installation on West Elevation.

## NEXT WEEK – 4.19.2021 – 4.23.2021

- Continue MEP overhead and trim out on Third, and Fourth floors of the new addition.
- Installing lights and Low-Voltage fixtures.
- Continue hardscapes on the East and South East Elevations. Begin prep for North Elevations.
- Continue Patio Roofing system.
- Continue Ceramic Tile Installation in Restrooms.
- Continue Metal Panel Installation.
- Continue Epoxy flooring in New Addition Restrooms.
- Continue Terrazzo Installation on Second Floor of New Addition Building.
- Continue VCT and Flooring Finishes in new Addition Building.



# Budget & Schedule

## BUDGET

Construction Budget

- \$34,900,000.00

Budget Status

- \$ 27,826,691.43

## SCHEDULE

Completion Date

- July 29,2021

Schedule Status

- On Schedule



## ADDITIONAL INFO

- Scheduled Substantial Completion Date
  - July 29, 2021
- Completed By
  - Will Henry, PCG
- Copies To
  - Danny Gutlay, APS
  - Sandra Horton, APS
  - Katy Daugharty, CC
  - Bob Just, CC
  - Jim Fallon, PCG
  - Alex Johnson, PCG
  - Will Henry, PCG
  - Art Cofelice, PCG
  - Travis Disbro, PCG
  - Tyler Cobb, PCG
  - Paul Cobb, PCG



# Photo Updates

## New Addition Progress – Southwest Elevation





## New Addition Progress – North Elevation



# Photo Updates

## Terrazzo Progress 2<sup>nd</sup> Floor of New Addition

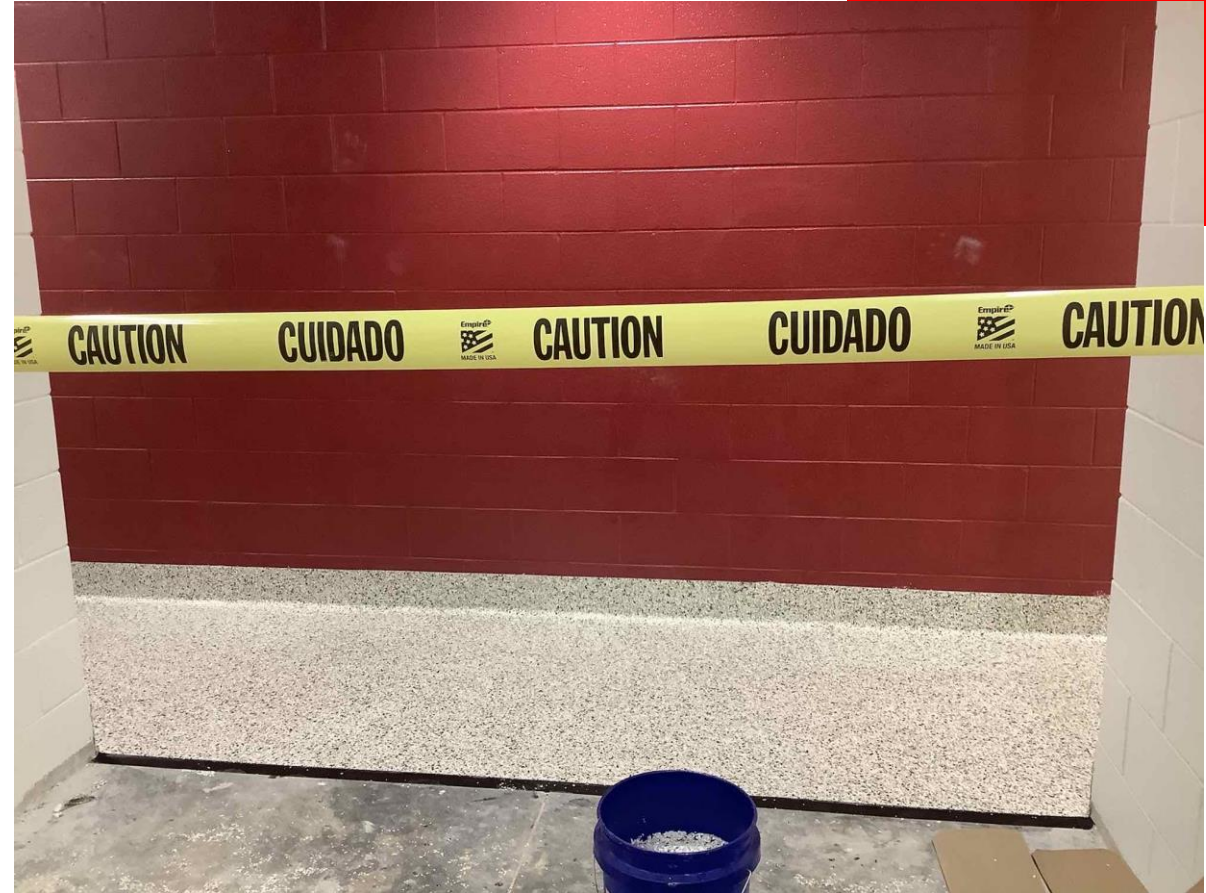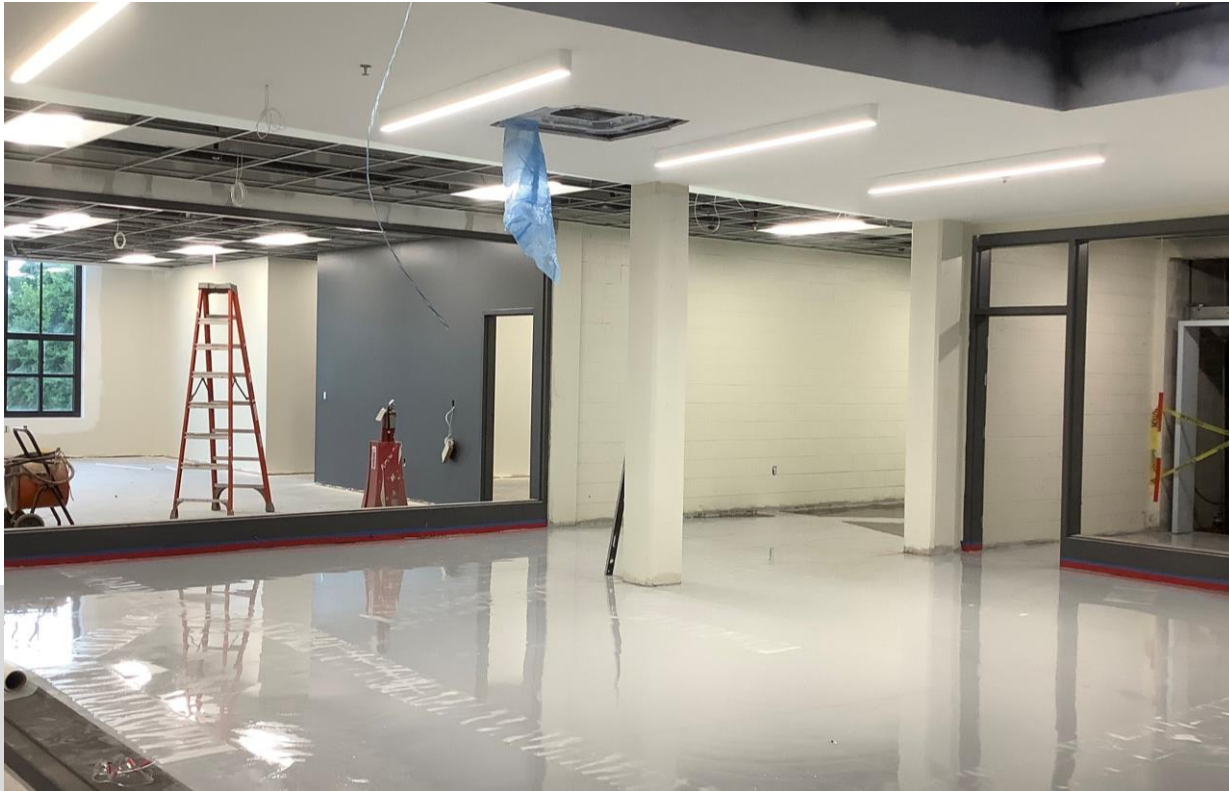


Epoxy Installed in New Addition Restrooms



# Photo Updates

## New Addition Restroom Progress

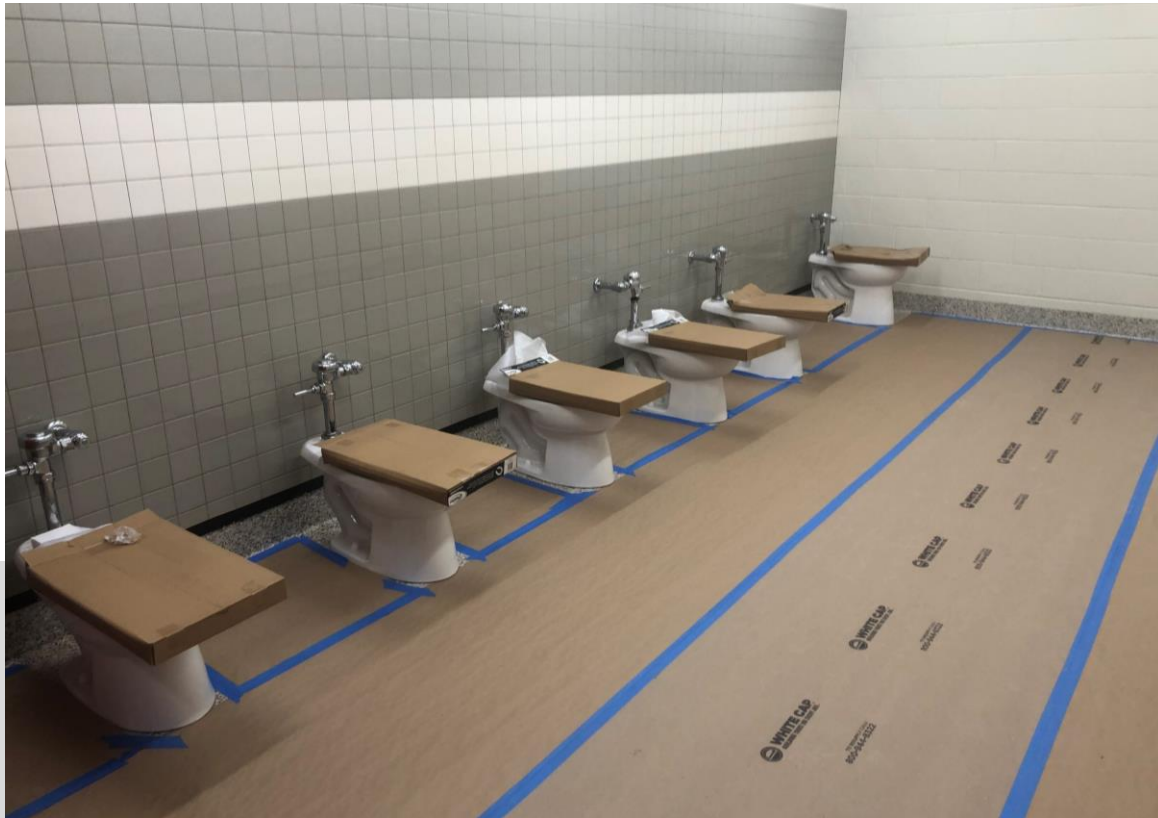

## New Addition Restroom Progress



# Photo Updates

North Elevation Metal Panel and Storefront Progress



VCT Installed in 4<sup>th</sup> Floor Classrooms  
of New Addition

