



Description

Concrete Masonry Unit Wall Installation Area D Hallway

Taken Date

05/02/2025 at 01:22 pm

Uploaded By

Kasey Sterling

Upload Date

05/02/2025 at 01:22 pm

File Name

[477176B2-6DB0-4CB6-B4E6-455...](#)

Album

Daily Logs



Description

Epoxy Flooring Installation in Area A Boy's Restroom

Taken Date

05/02/2025 at 01:13 pm

Uploaded By

Kasey Sterling

Upload Date


05/02/2025 at 01:21 pm

File Name

[9F143B76-7809-449B-85F6-FABA...](#)

Album

Daily Logs

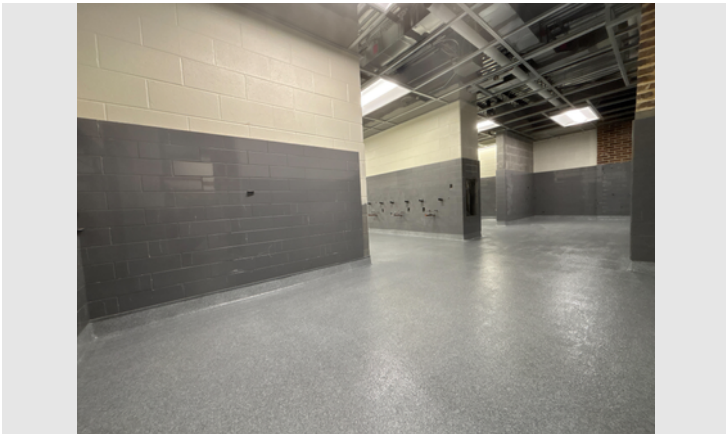

Description

Epoxy Flooring Installation in Area A Girl's Restroom

Taken Date

05/02/2025 at 01:13 pm

Uploaded By

Kasey Sterling

Upload Date


05/02/2025 at 01:21 pm

File Name

[C605932B-CCD1-48ED-AE60-EA3...](#)

Album

Daily Logs

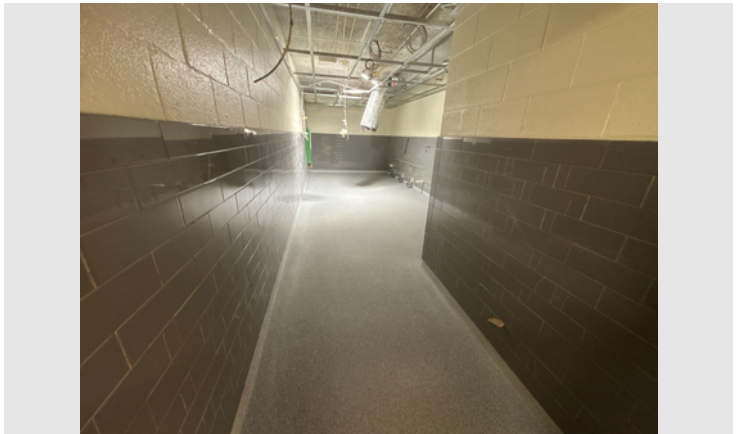

Description

Epoxy Flooring Installation in Area B Boy's Restroom

Taken Date

05/01/2025 at 03:26 pm

Uploaded By

Kasey Sterling

Upload Date

05/02/2025 at 05:17 am

File Name

[AC032DA2-4657-4DFB-B876-353...](#)

Album

Daily Logs

WEEKLY PROGRESS UPDATE REPORT

KIPP Vision Elementary

04/28/25 – 05/02/25



Last Week's Activities:

- Start plumbing fixture install – Area A
- Start water heater install – Area B
- Start duct installation – Area D
- Start gutter install – Area E
- Start concrete demolition – Area D Exterior
- Start sidewalk demolition – East Parking
- Start sidewalk demolition – West Parking
- Start flagpole install – Bus Lane
- Complete ceiling framing installation – Area B
- Complete existing HVAC demolition – Area B
- Complete sanitary in wall rough – Area D
- Complete overhead plumbing rough – Area D

This Week's Activities:

- Start masonry unit walls – Area D
- Continued electrical in wall rough – Area D
- Continue water heater installation – Area B
- Continue water heater installation – Area C
- Continue gutter install – Area E
- Complete epoxy flooring – Area A
- Complete epoxy flooring – Area B
- Complete epoxy flooring – Area C
- Complete concrete pour back – Area D Exterior
- Complete storm sewer installation – Courtyard
- Complete sidewalk pour back – East Parking
- Complete sidewalk pour back – West Parking

Next Week's Activities:

- Start masonry brick wall at courtyard wall – Area B
- Start masonry brick wall – Dumpster Enclosure
- Start masonry wall – Area A to D Hallway
- Start drywall ceiling – Area A
- Start drywall ceiling – Area B
- Start drywall ceiling – Area C
- Continue steel install – Area D
- Complete masonry unit walls – Area D

WEEKLY PROGRESS UPDATE REPORT

KIPP Vision Elementary

04/28/25 – 05/02/25



<u>Contract and Billings</u>	
Contract	
Current Contract Value	\$5,297,682.00
Billings	
Date Last Billing Submitted	3/28/2025
Total Billed to Date (Including Retainage)	\$2,886,924.92
Date of Last Payment	2/24/2025
Amount Paid to Date	\$952,036
Amount Open Receivables (Not Including Retainage)	\$1,883,109.78
Percent Billed to Date	54%
