


## WEEKLY CONSTRUCTION PROGRESS REPORT

### Project name: Northwest Bus Transit Center

WEEK ENDING 02/16/2024

Initial information	Data
PROJECT BUDGET (GMP)	\$19,664,171.00
START DATE	09/19/2023
COMPLETION DATE	07/31/2024
NAME OF THE CMAR	AJAX BUILDING COMPANY
PROJECT MANAGER FROM CMAR	LAMONT EAKINS
PROJECT MANAGER FROM APS	ALEX REVIN
PREPARED BY	SHYHEIM HOWARD

#### PROJECT OVERVIEW

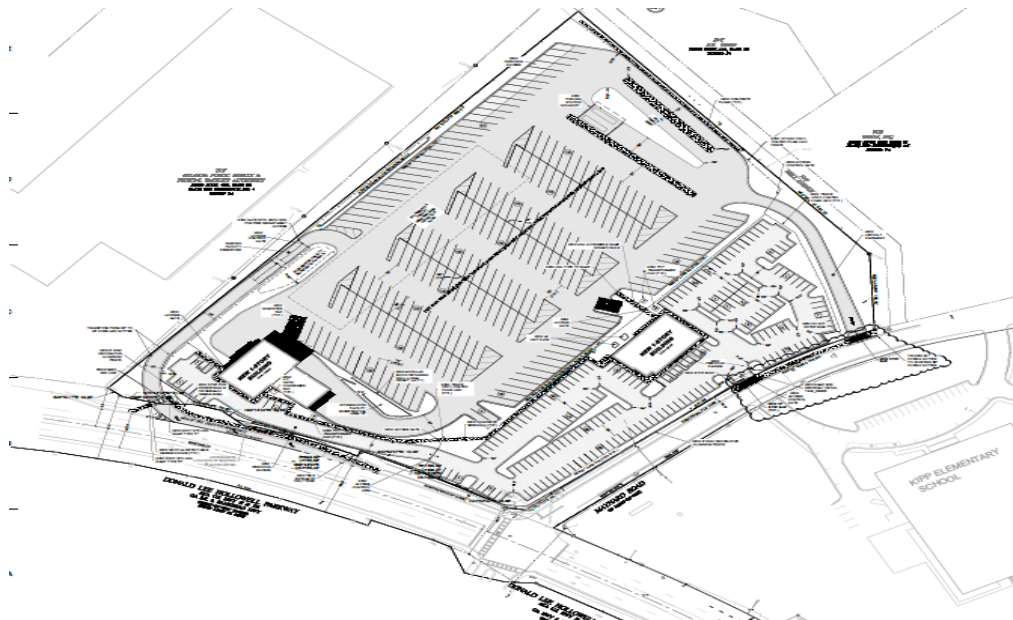

### Construction Activities this week

---

- CONCRETE PIERS/SPREAD FOOTINGS POURS ARE ONGOING AT MAINTENANCE BUILDING.
- ELECTRICAL/PLUMBING UNDERGROUND ROUGH-INS ARE 100% COMPLETED AT OPERATIONS BUILDING.
- OIL/GRIT SEPARATOR HAS MADE IT ONSITE. CURRENTLY BEING INSTALLED. CMP SLOT DRAIN WILL ARRIVE ONSITE WEEK OF (02/23/24).
- GDOT PERMIT IS IN FINAL STAGES OF PROCESSING.
- 100% OF MASS GRADING FOR LAYDOWN AREA IS COMPLETE. EQUIPMENT AND CONEX BOXES HAVE ARRIVED ONSITE. GRAVEL HAS BEEN LAID.
- SANITARY PIPING IS ROUGHLY 50 % INSTALLED UNDERGROUND.
- FIRE LINE/DOMESTIC WATER LINE LOOP INS ARE ONGOING AT OPERATION BUILDING PAD.
- MODULAR BLOCK HAS ARRIVED ONSITE (02/15/24). PLEASE SEE PICTURES BELOW FOR REFERENCE. INSTALLATION WILL OCCUR WEEK OF (02/23/24)
- OPERATIONS BUILDING SLAB POUR BACK OCCURRED ON FRIDAY AT 5:00 A.M (02/16/24). PLEASE SEE PICTURES BELOW FOR REFERENCE.
- REBAR IS IN THE PROCESS OF BEING INSTALLED AT MAINTENANCE BUILDING WEEK OF (02/16/24).

### CONSTRUCTION ACTIVITIES PLANNED (5 WEEK LOOK AHEAD)

#### **THIS IS DEPENDENT UPON PERMITTING STATUS AND WEATHER.**

- CONCRETE, PLUMBING & ELECTRICAL EQUIPMENT DELIVERIES WILL CONTINUE WEEK OF (02/23/24)
- STRUCTURAL FOUNDATION LAYOUT
- UNDERSLAB MEP INSTALLATION ARE ONGOING AT MAINTENANCE BUILDING WEEK OF (02/23/24)
- MAINTENANCE BUILDING SLAB POURED TRACKING FOR WEEK OF (02/29/24) DUE TO WEATHER AND SITE CONDITIONS.
- SANITARY & WATER UTILITIES SCOPE OF WORK CONTINUED.

## WEEKLY CONSTRUCTION PROGRESS REPORT



### MANPOWER LOG (WEEK OF 02/16/24)

SUBCONTRACTOR	M	T	W	TH	F
LEWIS CONTRACTING	20	20	20	20	20
JAMISON CONSTRUCTION	6	6	6	6	6
PENCO ELECTRICAL	3	3	3	3	3
TEBARCO MECHANICAL	3	3	3	3	3
NOVA ENGINEERING	1	1	1	1	1

### WEATHER LOG (MONTH OF DECEMBER/JANUARY/FEBRUARY)

- UP TO DATE, APS NW TRANSPORTATION CENTER HAS HAD (25) TWENTY-FIVE TRACKED RAIN DAYS IN DECEMBER/JANUARY/FEBRUARY.
- DAYS LOGGED: (12-01-23) / (12-02-23) / (12-03-23) / (12-08-23) / (12-09-23) / (12-10-23) / (12-24-23) / (12-25-23) / (12-26-23) / (01/06/24) / (01/08/24) / (01/09/24) / (01/12/24) / (01/16/24) / (01/19/24) / (01/24/24) / (01/25/24) / (01/26/24) / (01/27/24) / (01/28/24) / (01/29/24) / (02/04/24) / (02/10/24) / (02/11/24) / (02/12/24)
- TRACKED INCLEMENT CONDITIONS DAYS: 30 DAYS



## WEEKLY CONSTRUCTION PROGRESS REPORT





## WEEKLY CONSTRUCTION PROGRESS REPORT





## WEEKLY CONSTRUCTION PROGRESS REPORT

