

# MILES

## ELEMENTARY SCHOOL

*Weekly Construction Progress Report*  
*Week 10/20/2025 - 10/24/2025*



**Balfour Beatty**

## Current Activities 10/20/2025 - 10/24/2025

### **Weekly Progress Summary (Oct 20 – Oct 24, 2025)**

This week's construction activities reflect continued progress across both the interior and exterior of the building. On the exterior, crews completed the forming and pouring of new concrete sidewalks and ramps along multiple building elevations, followed by surface finishing and grading around the newly placed concrete. Preparations also continued for additional site concrete and landscaping work in upcoming weeks. Inside the building, ceiling grid installations advanced throughout corridors and classrooms, accompanied by ongoing MEP overhead coordination including lighting, ductwork, and sprinkler head placement. Subfloor preparation continued in select corridors, while cleanup efforts were performed in several classrooms to support inspection readiness. Overall, the project continues to maintain steady momentum, with visible progress across key scopes as the team transitions from rough-in to finish-phase activities.

#### **Key Deliverables**

- NG Generator - 12/15/25
- ERUs - 9/26/25 (Delivered and Staged off site)



**LORD AECK SARGENT**

**Balfour Beatty**




**Exterior Improvements**



**Interior Improvements**

## Progress Photos

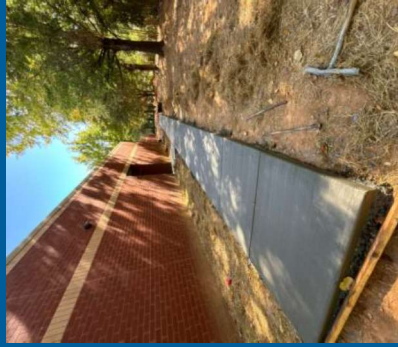

## Project Schedule

- Schedule Status: On Schedule



## Project Financials

- Construction GMP: \$10,528,700.00
- Progress Billed to Date: \$5,485,998.10 = 52.10% Completion
- Budget Status: Within GMP



**Balfour Beatty**
