


*Quote of the week: "You must be the change you wish to see in the world ."*

## Project: FL Stanton ES Renovation and addition

**Week ending: February 2, 2024**

- Continue fire sprinkler install in the gym
- Begin constructing retaining walls
- Begin Sanitary sewer install
- Begin covering up bathroom ceilings
- Begin installing structural HVAC unit Platforms on roof
- Completed new kitchen addition exterior CMU blk wall install
- Begin installing trap primers

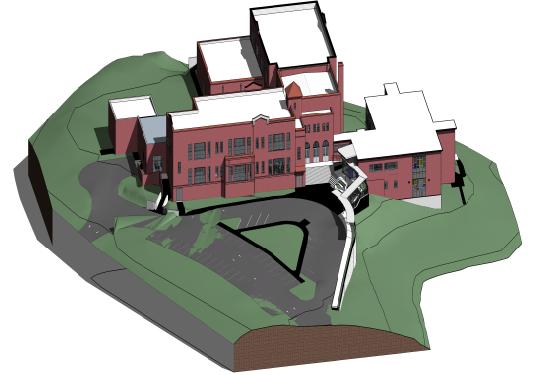

*Hard ceiling framing in the bathrooms is complete.*



*Sanitary sewer line has been set in place*



*Began forming up retaining walls at the courtyard area.*



*Continue exterior glass removable.*

## **NEXT WEEK – February 5 - February 9**

- Complete all blocking throughout
- Begin setting all HVAC rooftop Units
- Pour footing for retaining walls
- Begin to set the Helical Piers for the 1928 building
- Complete hard ceiling install in the bathrooms
- Begin interior painting

## **SCHEDULED DATE OF SUBSTANTIAL COMPLETION**

- June 30 , 2024

## **Final Completion**

- June 30, 2024

## **PREPARED BY:**

Jahaziel Lee, Carroll Daniel Construction Co.
