


Quote of the week: "Don't be intimidated by what you don't know. That can be your greatest strength and ensure that you do things differently from everyone else."


Project: FL Stanton ES Renovation and Addition

Week ending: June 7, 2024

- Begin generator install
- Installed transformer pad
- Begin exterior paint work
- Begin basement level VCT install
- Begin modular wall work
- Begin asphalt paving
- Continue installing exterior windows

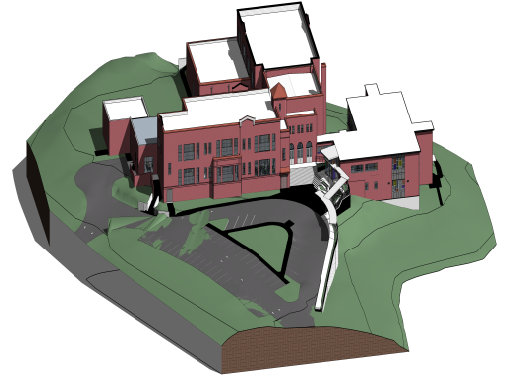

Begin Modular wall work

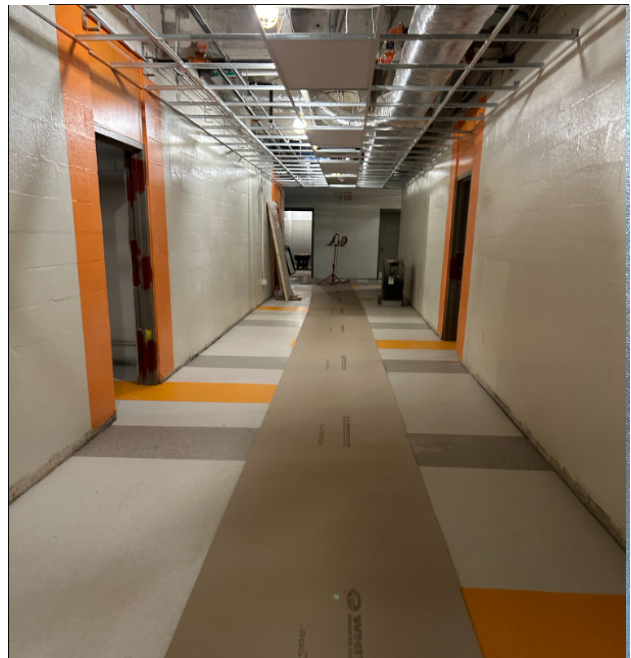

1958 VCT floor install is complete



Installing balcony grates



Water fountain install is complete

NEXT WEEK – June 10 - June 14

- Begin storm water box relocation
- Begin relocating transformer - Georgia Power
- Continue with Asphalt paving work
- Continue with sidewalk forming and pouring
- Begin landscape install
- Began installing wall pads in the gym.
- Begin boring to the monument sign
- Begin installing LED Message board

SCHEDULED DATE OF SUBSTANTIAL COMPLETION

- June 30 , 2024

Final Completion

- June 30, 2024

PREPARED BY:

Jahaziel Lee, Carroll Daniel Construction Co.
