


Quote of the week: "Great things happen to those who don't stop believing, trying, learning, and being grateful."

Project: FL Stanton ES Renovation and addition

Week ending: February 9, 2024

- Continued plumbing rough in the kitchen
- Continued fire sprinkler rough -in
- Poured loading dock walls
- Dug and poured retaining wall footings
- Completed CMU in the kitchen
- Framed restroom ceilings
- Passed electrical and framing wall cover up inspections
- Begin installing roof curb framing
- Completed plaster in 1928 Classrooms
- Begin hanging hollow metal doors
- Started removing windows
- Installing roof curbs and equipment rails

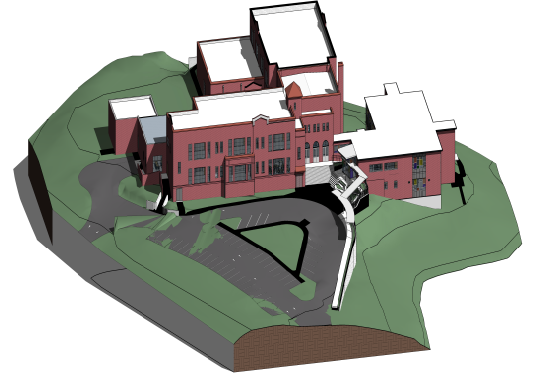

Continue to install joist and deck at the new kitchen addition



Continue constructing retaining walls



Began waterproofing at the 1958 building



Continue installing roof rail curbs

NEXT WEEK – February 12 - February 16

- Install decking at the media center
- Pour slab at the media center
- Pour retaining wall
- Install fluid-applied air weather barrier at kitchen addition and 1958 wing
- Begin water proofing at the front stairs
- Grading at security vestibule and front stairs
- Begin hanging drywall
- Complete all soffit in corridors
- Begin pouring security vestibule footings and slabs
- Begin joist & deck install at the kitchen addition
- Complete opening reinforcements at the new cafeteria

SCHEDULED DATE OF SUBSTANTIAL COMPLETION

- June 30 , 2024

Final Completion

- June 30, 2024

PREPARED BY:

Jahaziel Lee, Carroll Daniel Construction Co.
