


Quote of the week: "Never give up on a dream just because of the time it will take to accomplish it. The time will pass anyways. "

Project: FL Stanton ES Renovation and Addition

Week ending: March 8, 2024

- Continue hanging drywall throughout
- Begin underground electrical rough in for generator pad, fire pump room , & electrical room
- Continue waterproofing at the front stairs
- Continue installing brick at the new kitchen addition
- Continue Patching brick at windows , openings, louvers, etc
- Complete all soffit's in the corridor areas
- Complete duct installation in the gym
- Continue plaster repair throughout

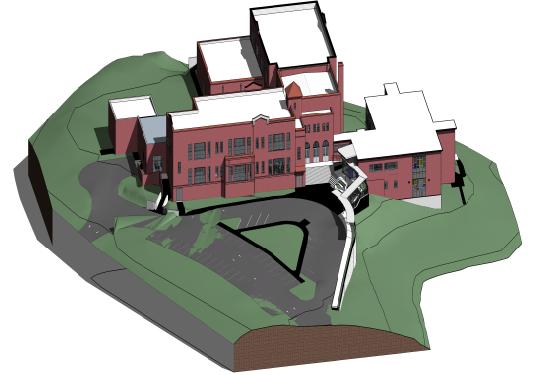

Continue with front detention pond install



Begin installing hollow metal doors throughout



*Will begin backfilling retaining wall
once the water dries up*



*Finish installing brick at the new
kitchen addition*

NEXT WEEK – March 11 - March 15

- Install decking at the media center
- Pour slab at the media center
- Form up stairs cases at loading dock and front entrances
- Continue grading at security vestibule and front staircase
- Complete roof curb framing and roof curb install
- Form and pour retaining wall at the entrances
- Construct footing for the monument sign
- Demo duct bank for completion of storm sewer system
- Begin grading and enlarging pond

SCHEDULED DATE OF SUBSTANTIAL COMPLETION

- June 30 , 2024

Final Completion

- June 30, 2024

PREPARED BY:

Jahaziel Lee, Carroll Daniel Construction Co.
