


WEEKLY CONSTRUCTION PROGRESS REPORT

Project name: Northwest Bus Transit center

WEEK ENDING 09/29/2023

Initial information	Data
PROJECT BUDGET (GMP)	\$19,664,171.00
START DATE	09/19/2023
COMPLETION DATE	07/31/2024
NAME OF THE CMAR	AJAX BUILDING COMPANY
PROJECT MANAGER FROM CMAR	LAMONT EAKINS
PROJECT MANAGER FROM APS	ALEX REVIN
PREPARED BY	LAMONT EAKINS

PROJECT OVERVIEW

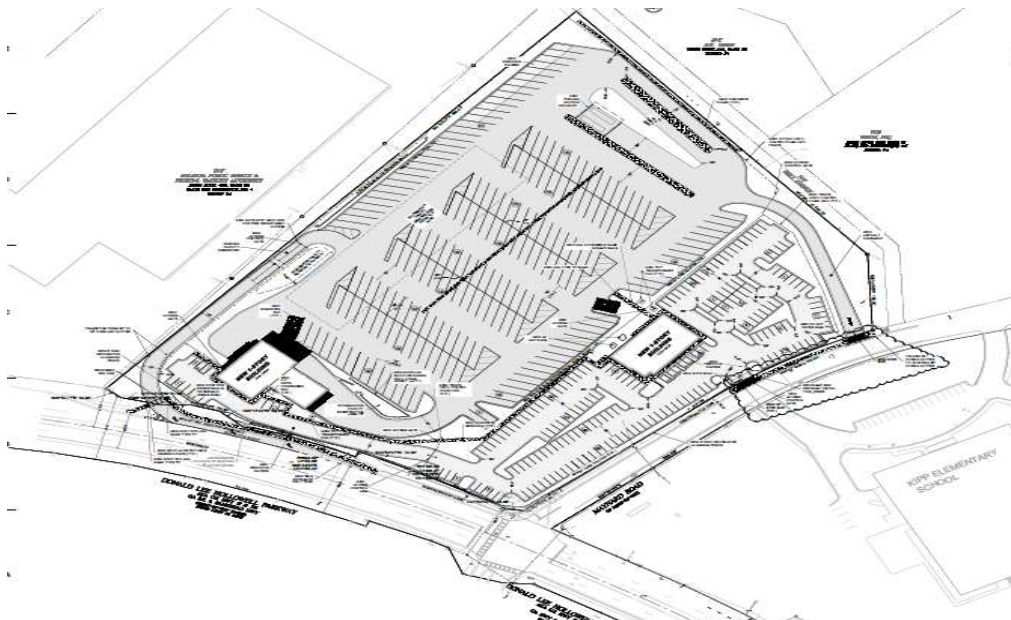

Construction Activities this week

- COMPLETED INSTALLATION OF TEMPORARY JOB SITE FENCE AND GATES
- STARTED INSTALLATION OF INITIAL PHASE OF EROSION CONTROL
- MOBILIZED SITE CLEARING EQUIPMENT TO THE SITE
- RECEIVED DELIVERY OF JOB TRAILER AND BEGAN SETUP

CONSTRUCTION ACTIVITIES PLANNED NEXT WEEK

- CALL IN 7 DAY EROSION CONTROL INSPECTION
- BEGIN SITE CLEARING AND GRUBBING
- COMPLETE SETUP OF JOBSITE TRAILER

WEEKLY CONSTRUCTION PROGRESS REPORT



WEEKLY CONSTRUCTION PROGRESS REPORT

