


WEEKLY CONSTRUCTION PROGRESS REPORT

Project name: Northwest Bus Transit center

WEEK ENDING 10/27/2023

Initial information	Data
PROJECT BUDGET (GMP)	\$19,664,171.00
START DATE	09/19/2023
COMPLETION DATE	07/31/2024
NAME OF THE CMAR	AJAX BUILDING COMPANY
PROJECT MANAGER FROM CMAR	LAMONT EAKINS
PROJECT MANAGER FROM APS	ALEX REVIN
PREPARED BY	SHYHEIM HOWARD

PROJECT OVERVIEW

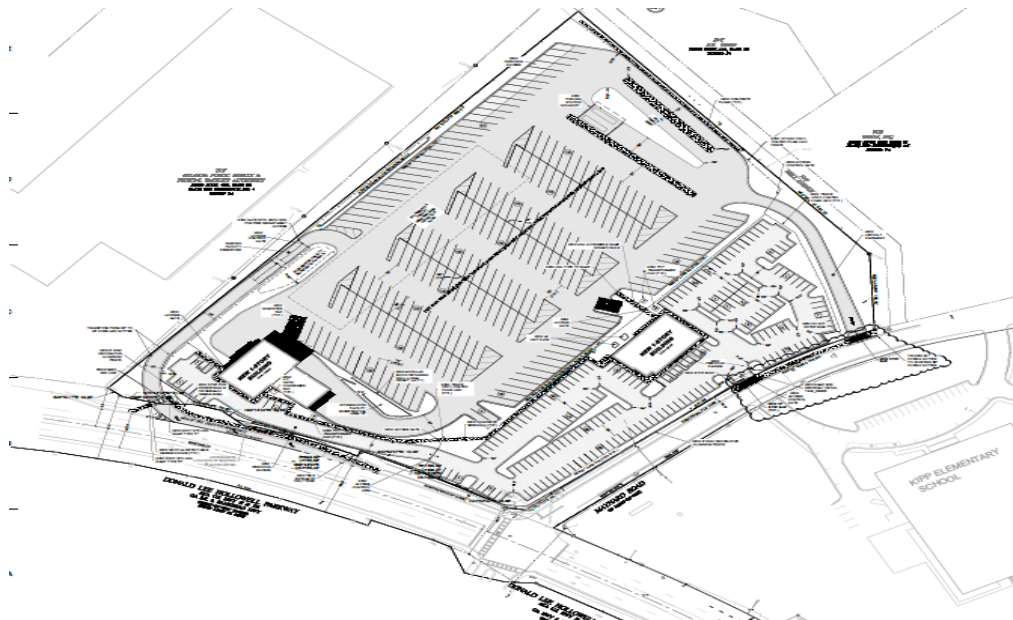

Construction Activities this week

- CLEARING/GRUBBING AND DEFORESTATION OF THE PROJECT JOBSITE HAS BEEN COMPLETED
- JOBSITE TRAILER HAS POWER CONNECTED, INTERNET & PLUMBING
- SITE UTILITIES MATERIAL DELIVERIES HAVE BEGUN
- CONTROL POINTS INSTALLED AND ESTABLISHED
- GRADING OF THE JOBSITE HAS BEGUN.

CONSTRUCTION ACTIVITIES PLANNED NEXT WEEK

- SITE GRADING WILL BE CONTINUED
- SITE UTILITY LAYOUT AND INSTALL IS TO BEGIN

MANPOWER LOG (WEEK OF 10/27/23)

- A TOTAL OF 45 INDIVIDUALS HAVE BEEN ONSITE
- AVERAGE OF 10 PEOPLE A DAY ONSITE

WEEKLY CONSTRUCTION PROGRESS REPORT



WEEKLY CONSTRUCTION PROGRESS REPORT

