


## WEEKLY CONSTRUCTION PROGRESS REPORT

### Project name: Northwest Bus Transit center

WEEK ENDING 11/03/2023

Initial information	Data
PROJECT BUDGET (GMP)	\$19,664,171.00
START DATE	09/19/2023
COMPLETION DATE	07/31/2024
NAME OF THE CMAR	AJAX BUILDING COMPANY
PROJECT MANAGER FROM CMAR	LAMONT EAKINS
PROJECT MANAGER FROM APS	ALEX REVIN
PREPARED BY	SHYHEIM HOWARD

### PROJECT OVERVIEW

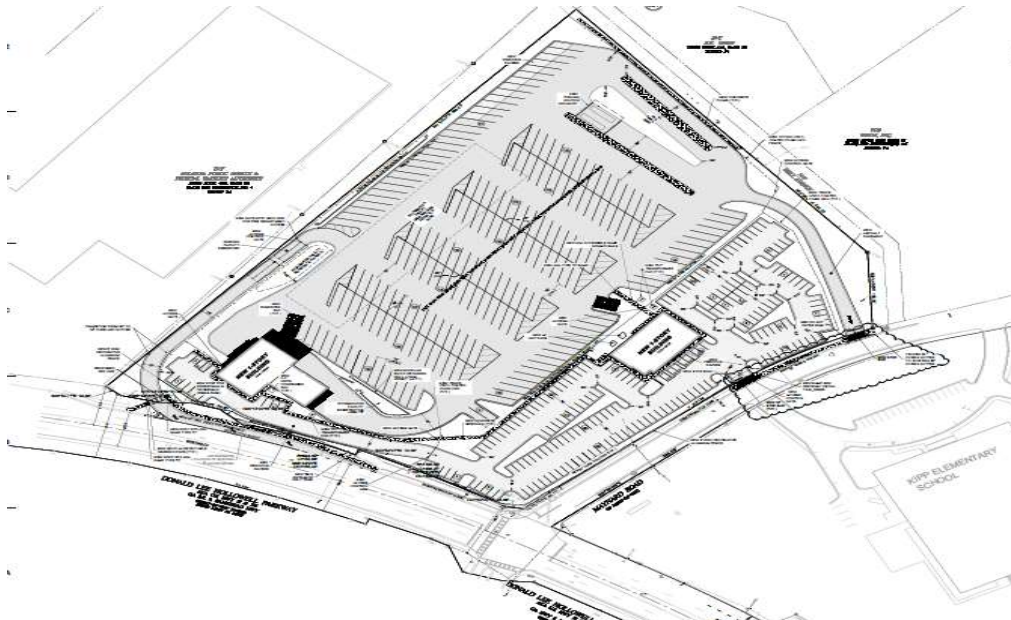

## WEEKLY CONSTRUCTION PROGRESS REPORT



### Construction Activities this week

- CLEARING/GRUBBING AND DEFORESTATION OF THE PROJECT JOBSITE HAS BEEN COMPLETED
- SITE UTILITIES MATERIAL DELIVERIES HAVE BEGUN
- GRADING OF THE JOBSITE IS STILL IN PROGRESS
- WORKING ON BUILDING PADS
- STARTING ON THE DETENTION POND

### CONSTRUCTION ACTIVITIES PLANNED NEXT WEEK

- SITE GRADING WILL BE CONTINUED
- SITE UTILITY LAYOUT AND INSTALL IS TO BEGIN
- CONTINUE TO WORK ON BUILDING PADS
- BEGINNING SANITARY SEWER TIE END

### MANPOWER LOG (WEEK OF 11/03/23)

SUBCONTRACTOR	M	T	W	TH	F
LEWIS CONTRACTING	10	15	15	15	10



## WEEKLY CONSTRUCTION PROGRESS REPORT

---





## WEEKLY CONSTRUCTION PROGRESS REPORT

---

