


WEEKLY CONSTRUCTION PROGRESS REPORT

Project name: Northwest Bus Transit center

WEEK ENDING 12/15/2023

Initial information	Data
PROJECT BUDGET (GMP)	\$19,664,171.00
START DATE	09/19/2023
COMPLETION DATE	07/31/2024
NAME OF THE CMAR	AJAX BUILDING COMPANY
PROJECT MANAGER FROM CMAR	LAMONT EAKINS
PROJECT MANAGER FROM APS	ALEX REVIN
PREPARED BY	SHYHEIM HOWARD

PROJECT OVERVIEW

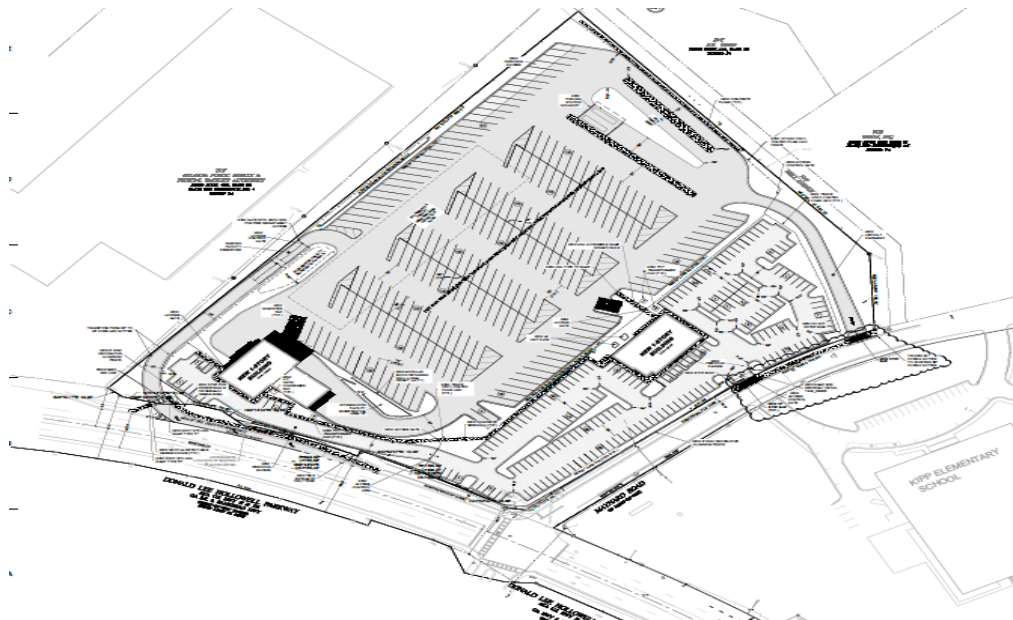

WEEKLY CONSTRUCTION PROGRESS REPORT



Construction Activities this week

- 80% COMPLETED WITH BIORETENTION
- 60% COMPLETED WITH STORM LINES/STRUCTURES
- OPERATIONS BUILDING PAD PREP. 80% COMPLETED
- COORDINATING A LOGISTICS PLAN FOR SS BORE ACROSS MAYNARD STREET
- EXCAVATING THE RETENTION BASIN.
- UNDERGROUND RETENTION SITE PREP
- MASS GRADING FOR LAYDOWN AREA. 65% COMPLETED

CONSTRUCTION ACTIVITIES PLANNED (5 WEEK LOOK AHEAD)

THIS IS DEPENDENT UPON BUILDING PERMIT STATUS AND WEATHER.

- CONCRETE, REBAR, PLUMBING & ELECTRICAL EQUIPMENT DELIVERIES
- STRUCTURAL FOUNDATION LAYOUT
- CONTINUE TO WORK ON BUILDING PADS
- UNDERSLAB PLUMBING INSTALLATION (MEP INSTALLATION)
- CONCRETE WORK/POUR SLABS
- SANITARY & WATER UTILITIES SCOPE OF WORK CONTINUED.

MANPOWER LOG (WEEK OF 12/15/23)

SUBCONTRACTOR	M	T	W	TH	F
LEWIS CONTRACTING	14	15	16	18	20

WEATHER LOG (MONTH OF DECEMBER)

- UP TO DATE, APS NW TRANSPORTATION CENTER HAS HAD (6) SIX TRACKED RAIN DAYS IN DECEMBER.
- DAYS LOGGED: (12-01-23) / (12-02-23) / (12-03-23) / (12-08-23) / (12-09-23) / (12-10-23)
- TOTAL RAINFALL/PRECIPITATION AMOUNT: 5-1/8" THUS FAR.
- AVERAGE RECOVERY TIME: 2-3 DAYS

WEEKLY CONSTRUCTION PROGRESS REPORT



WEEKLY CONSTRUCTION PROGRESS REPORT

