


WEEKLY CONSTRUCTION PROGRESS REPORT

Project name: Northwest Bus Transit center

WEEK ENDING 12/22/2023

Initial information	Data
PROJECT BUDGET (GMP)	\$19,664,171.00
START DATE	09/19/2023
COMPLETION DATE	07/31/2024
NAME OF THE CMAR	AJAX BUILDING COMPANY
PROJECT MANAGER FROM CMAR	LAMONT EAKINS
PROJECT MANAGER FROM APS	ALEX REVIN
PREPARED BY	SHYHEIM HOWARD

PROJECT OVERVIEW

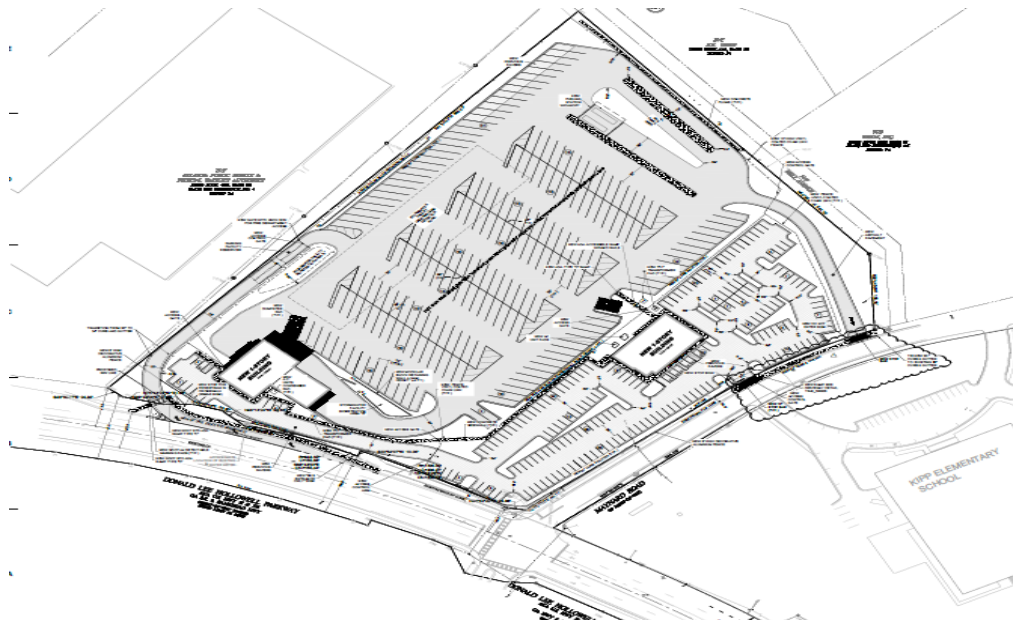

WEEKLY CONSTRUCTION PROGRESS REPORT



Construction Activities this week

- 90% OF CMP HAS BEEN SET IN THE RETENTION POND. TRACKING TO BE COMPLETED END OF NEXT WEEK.
- 70% COMPLETED WITH STORM LINES/STRUCTURES
- 100% COMPLETED WITH OPERATIONS BUILDING PAD
- 100% COMPLETED WITH MAINTENANCE BUILDING PAD. GRAVEL NEEDS TO BE LAID.
- COORDINATING A LOGISTICS PLAN FOR SS BORE ACROSS MAYNARD STREET. SITE CONTRACTOR HAS BEEN ABLE TO LOCATE AND SIGN UP A JACK & BORE COMPANY.
- EXCAVATING THE RETENTION BASIN.
- UNDERGROUND RETENTION SITE PREP
- 100% OF MASS GRADING FOR LAYDOWN AREA IS COMPLETE. GRAVEL NEEDS TO BE LAID.

CONSTRUCTION ACTIVITIES PLANNED (5 WEEK LOOK AHEAD)

THIS IS DEPENDENT UPON BUILDING PERMIT STATUS AND WEATHER.

- CONCRETE, REBAR, PLUMBING & ELECTRICAL EQUIPMENT DELIVERIES
- STRUCTURAL FOUNDATION LAYOUT
- UNDERSLAB PLUMBING INSTALLATION (MEP INSTALLATION)
- CONCRETE WORK/POUR SLABS
- SANITARY & WATER UTILITIES SCOPE OF WORK CONTINUED.


MANPOWER LOG (WEEK OF 12/22/23)

SUBCONTRACTOR	M	T	W	TH	F
LEWIS CONTRACTING	16	16	16	16	15

WEATHER LOG (MONTH OF DECEMBER)

- UP TO DATE, APS NW TRANSPORTATION CENTER HAS HAD (6) SIX TRACKED RAIN DAYS IN DECEMBER.
- DAYS LOGGED: (12-01-23) / (12-02-23) / (12-03-23) / (12-08-23) / (12-09-23) / (12-10-23)
- TOTAL RAINFALL/PRECIPITATION AMOUNT: 5-1/8" THUS FAR.
- AVERAGE RECOVERY TIME: 2-3 DAYS
- NO RAIN TO REPORT FOR WEEK OF (12-22-23).

WEEKLY CONSTRUCTION PROGRESS REPORT

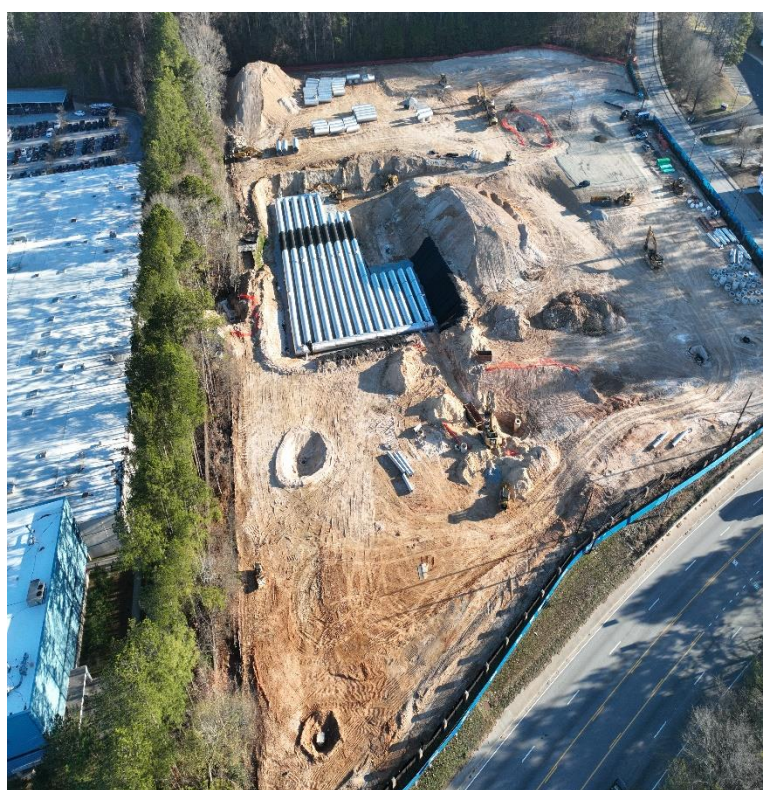

WEEKLY CONSTRUCTION PROGRESS REPORT

