



Weekly Construction Progress Report

Morningside Elementary School

Week Ending: 04/29/2022

THIS WEEK

- Painting continuing in the existing building
- Fire sprinkler installation continuing in Area C (new building)
- Mechanical, Electrical, and Plumbing rough-in continuing in new addition
- Ceiling tile installation continuing in existing building
- Lighting installation continuing in existing building
- Metal stud installation in new building continuing
- Drywall installation in new building continuing
- Exterior brick installation finishing
- Storefront framing and glazing installation continuing
- Plumbing fixture installation continuing in the existing building
- Flooring installation continuing in the existing building
- Interior handrail installation continuing
- Ceramic wall tile installation beginning in Area C

NEXT WEEK: 05.02.22 – 05.06.22

- Painting continuing in the existing building
- Fire sprinkler installation continuing in Area D
- Mechanical, Electrical, and Plumbing rough-in continuing in the new addition
- Ceiling tile installation continuing in existing building
- Lighting installation continuing in existing building
- Metal stud installation in new building continuing
- Drywall installation in new building continuing
- Storefront framing and glazing installation continuing
- Plumbing fixture installation continuing in the existing building
- Flooring installation continuing in the existing building
- Ceiling grid installation beginning in the new addition
- Interior handrail installation continuing
- Ceramic wall tile installation finishing in Area C
- Final grading beginning

BUDGET/SCHEDULE

Construction Budget

\$17,600,000.00

Budget Status

\$12,732,689.80

Substantial Completion:

July 25, 2022

Schedule Status:

On Schedule


Completed By:

Chris Hubbard

PARRISH
CONSTRUCTION GROUP

Photo/Activity Updates

Brick installation on Southwest stair tower

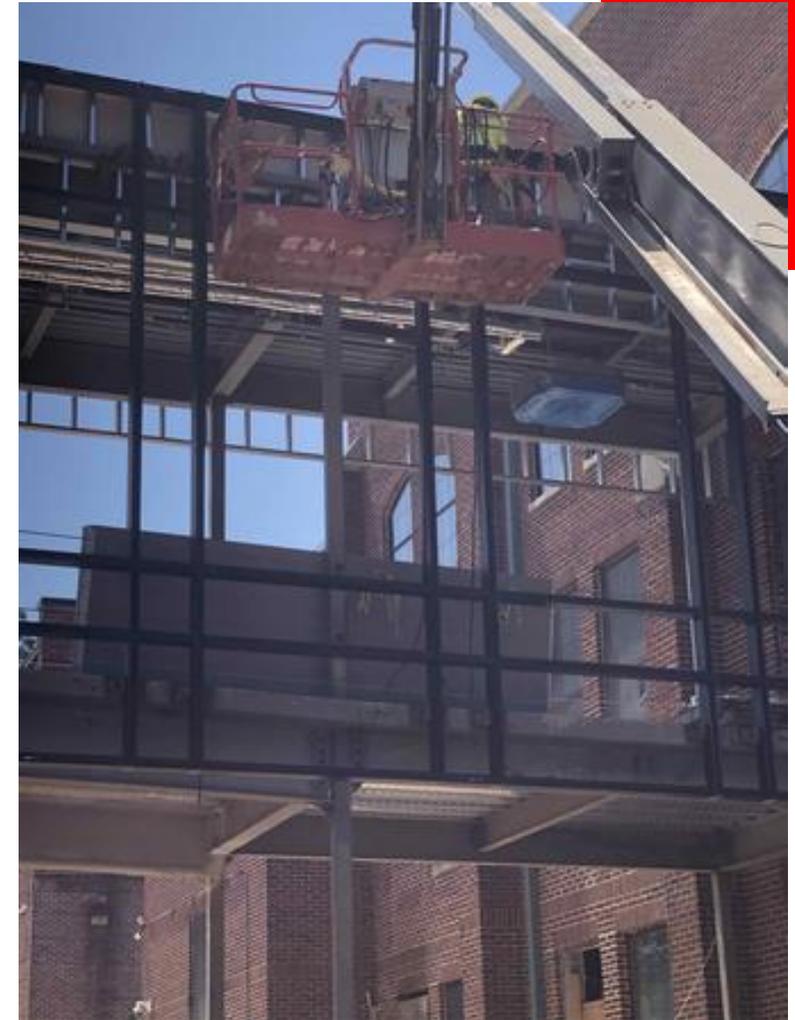


Storefront install at new bridge



Photo/Activity Updates

Handrail installation

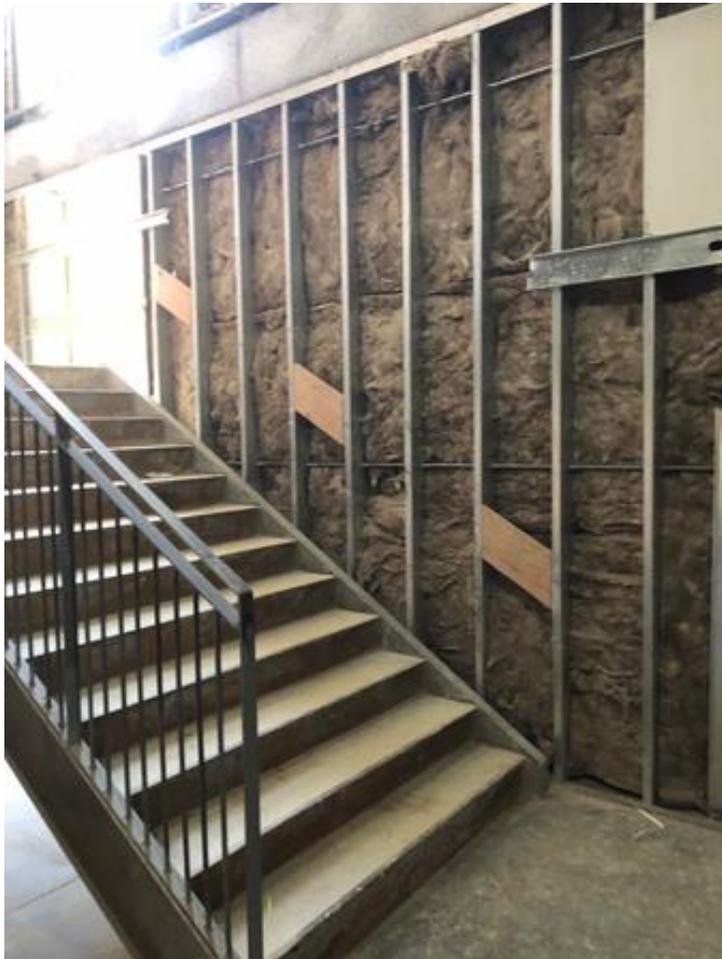

Gym drywall installation



Photo/Activity Updates

Painting in new building



Electrical panel rough-in



Photo/Activity Updates

Kitchen cooler/freezer installation



Ceramic wall tile in new building

