

**WEEKLY PHOTO REPORT**  
**APS Field House – Washington High School**  
April 22, 2022



**Prepared For:** Atlanta Public Schools

**Prepared By:** Tyler Cade




Building Pad Undercutting



Fabric Install



Undercut Backfill

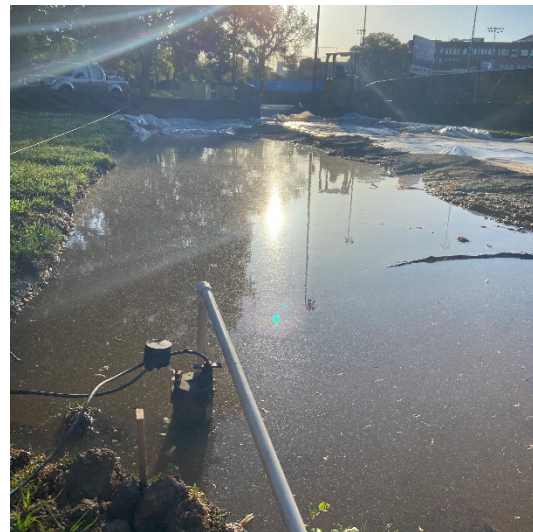

Building Pad Water Remediation

# WEEKLY PHOTO REPORT

## APS Field House – Washington High School



April 22, 2022

### Last Week's Activities:

- Continued clearing and grubbing
- Continued site access roads
- Continued grading layout
- Started subgrade inspections
- Started fence demolition
- Started temporary utilities
- Started underground utilities

### This Week's Activities:

- Continued clearing and grubbing
- Continued site access roads
- Continued grading layout
- Continued subgrade inspections
- Continued fence demolition
- Continued temporary utilities
- Continued underground utilities
- Started subgrade undercutting

### Next Week's Activities:

- Complete clearing and grubbing
- Complete fence demolition
- Complete site access roads
- Continue subgrade inspections
- Continue temporary utilities
- Continue underground utilities
- Start building pad structural fill
- Start subbase inspections
- Start under slab rough ins
- Start footings and slab on grade prep

Contract & Billings	
<b>Contract</b>	
Current Contract Value	\$1,519,162
<b>Billings</b>	
Date Last Billing Submitted	N/A
Total Billed to Date (Including Retainage)	\$0
Date of Last Payment	N/A
Amount Paid to Date	\$0
Amount Open Receivables (Not Including Retainage)	\$0
Percent Billed to Date	0%
