

History of the Week: Did you know that wattle & daub was a common wall-building method used across Europe, Asia, Africa, and the Americas? It involves weaving wooden stakes (wattles) with twigs and covering them with clay or mud (daub) to create weatherproof walls. In timber-framed structures, wattles are inserted into timber slots and plastered with clay. The lath-and-plaster method later evolved from this technique using standardized materials before drywall..(See pics below)

Project: Hank Aaron Academy Additions & Modifications

Week Ending: February 7, 2025

THIS WEEK:

- Building Pad is 90% complete
- Ongoing excavating and pouring footing
- Continuing MEP rough-in work in the cafeteria
- Began formwork for foundation wall



Installing and placing rebar and rebar mats in the footing



Pouring concrete in footing





Grading building pad





Ductwork installed in cafeteria

NEXT WEEK – February 10th -February 14th

- Complete building pad
- Complete gym footings
- Continue MEP rough-in, in the cafeteria
- Continue formwork for foundation wall

History Moment: Wattle & Daub

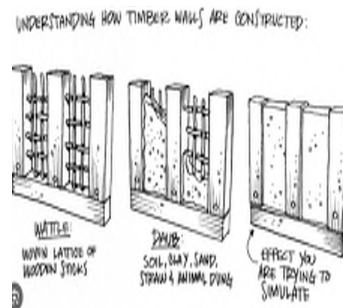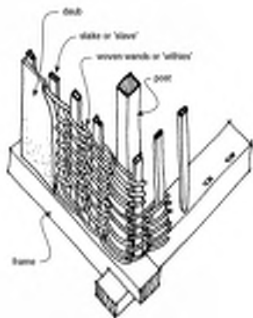

SCHEDULED DATE OF SUBSTANTIAL COMPLETION

- December 1, 2025

PREPARED BY:

Karee Shaw, Carroll Daniel Construction Co.

