


**Quote of the week:** ““You can use an eraser on the drafting table, or a sledgehammer on the construction site.” – Frank Lloyd Wright

## Project: Hank Aaron Academy Additions & Modifications

**Week Ending: December 27, 2024**

### THIS WEEK:

- Completed installation of pavers
- Started cafeteria demo

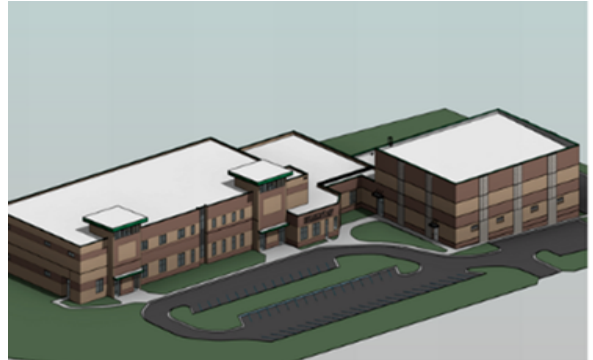

*Paver installation completed on the left side.*



*Paver installation completed on the right side.*





*Removing ceiling tile*



*Cafeteria demo in Progress*

### **NEXT WEEK – December 30th -January 3rd**

- Continue cafeteria demo
- Remove and relocate the temporary fence as per the logistics plan for Phase 2
- Start striping and signage for upper parking lot

### **SCHEDULED DATE OF SUBSTANTIAL COMPLETION**

- December 1, 2025

### **PREPARED BY:**

Karee Shaw, Carroll Daniel Construction Co.

