

History of the Week: Did you know, The Great Pyramid of Cholula, the largest by volume at 4.45 million cubic meters, is located near Puebla, Mexico. It was a major religious center in pre-Columbian times, with construction starting in the 2nd century BC. Today, it remains a significant archaeological and cultural site. (See pics below)

Project: Hank Aaron Academy Additions & Modifications


Week Ending: March 7, 2025

THIS WEEK:

- Weather delay: 1 day of rain
- Preparing for final slab
- Completed duct work in cafeteria
- EP rough-in work continues in cafeteria
- Continue backfilling
- CMU wall installation in progress in gym & cafeteria
- Ongoing underground plumbing



Grouting 8" block around stage walls

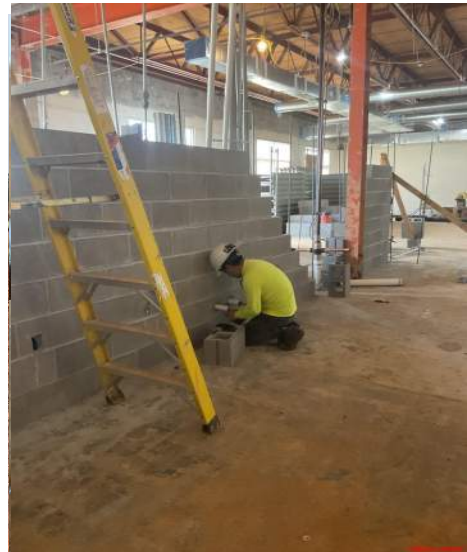

Plumbers installing pipe in CMU wall






Sanitary sewer installed under slab



Ductwork completed in cafeteria

NEXT WEEK – March 10 - March 14

- Pour slab at north end
- Continue backfilling & installing CMU walls
- Continue underground plumbing
- Start underground electrical work
- Continue EP rough-in work in cafeteria

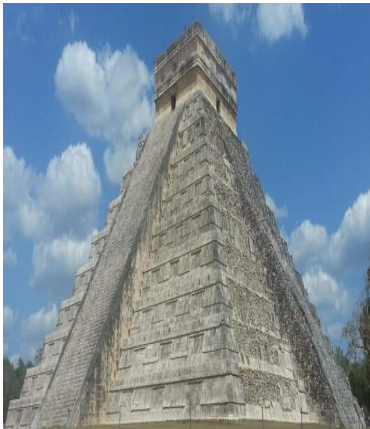

SCHEDULED DATE OF SUBSTANTIAL COMPLETION

- December 1, 2025

PREPARED BY:

Karee Shaw, Carroll Daniel Construction Co.

