

An aerial photograph of Grady High School and its stadium. The school buildings are on the left, and the large stadium with tiered seating is in the center. A football field is visible in the foreground. In the background, a dense forest separates the school from a city skyline with several tall skyscrapers under a clear sky.

Weekly Construction Progress Report

Grady High School

Week Ending: 10/16/2020

PARRISH
CONSTRUCTION GROUP

Weekly Updates

THIS WEEK

- MEP overhead on First Floor of new addition.
- MEP overhead on Second floor of new addition.
- Continue CMU install Second and Third Floor of new addition.
- Roof Decking Installed.
- Poured fourth floor column wraps of new addition.
- Continue Fire Sprinkler first floor.
- Piers poured for bridge connection.
- Plumbing Rough-in third and fourth floor.
- Exterior metal framing.
- Framing roof parapets.

NEXT WEEK – 10.19.2020 – 10.23.2020

- Continue CMU walls on second floor of new addition.
- Continue CMU walls on the third floor of the new addition.
- Continue MEP overhead and rough-in on First, Second, Third, and Fourth floors of the new addition.
- Steel Erection for Bridge Connection with Charles Allen Building.
- Complete Roof Decking install at new addition.
- Metal Framing on Second floor.
- Continue exterior metal framing.



Budget & Schedule

BUDGET

Construction Budget

- \$34,900,000.00

Budget Status

- \$ 15,149,982.76

SCHEDULE

Completion Date

- July 29,2021

Schedule Status

- On Schedule



ADDITIONAL INFO

- Scheduled Substantial Completion Date
 - July 29, 2021
- Completed By
 - Will Henry, PCG
- Copies To
 - Danny Gutlay, APS
 - Sandra Horton, APS
 - Katy Daugharty, CC
 - Bob Just, CC
 - John Rood, PCG
 - Darrell Bailey, PCG
 - Alex Johnson, PCG
 - Will Henry, PCG
 - Art Cofelice, PCG
 - Travis Disbro, PCG



Photo Updates

New Addition Progress



New Addition Progress



Photo Updates

Metal Framing Complete at High Roof of
The New Addition



Metal Framing Complete at High Roof of
The New Addition



Photo Updates

Selective Demo at Charles Allen Building for Bridge Tie-In



Walls installed at South East Exterior



Photo Updates

MEP Overhead Progress 4th Floor




New Curbs Formed at South Patio



Photo Updates

Rooftop Curbs set on High Roof
of New Addition

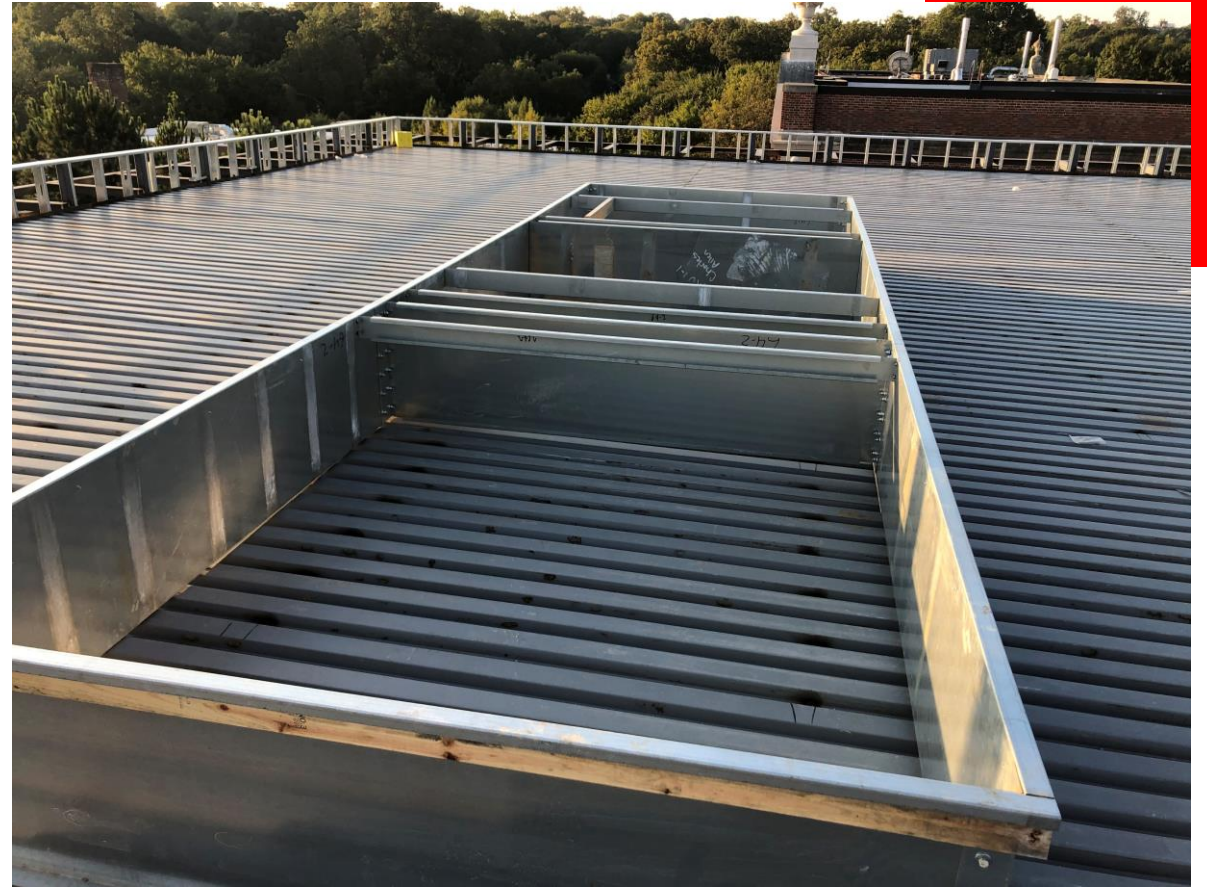

Rooftop Curbs set on High Roof of New
Addition

