

10th Street

8th Street

Charles Allen Drive

Monroe Drive

Demo &
Remove
Trailers

10 Temporary
Classrooms

Temporary Fence
Around Trailers As
Needed.


Sequence One

Sept. 2019 - Jan. 2020

Setup new trailers at the west side. Teachers occupy in December. Early Release of temporary parking, tree removal for trailers only

Remove all existing old trailers.

Community Outreach and distributing introductory project flyers to the surrounding neighbors.

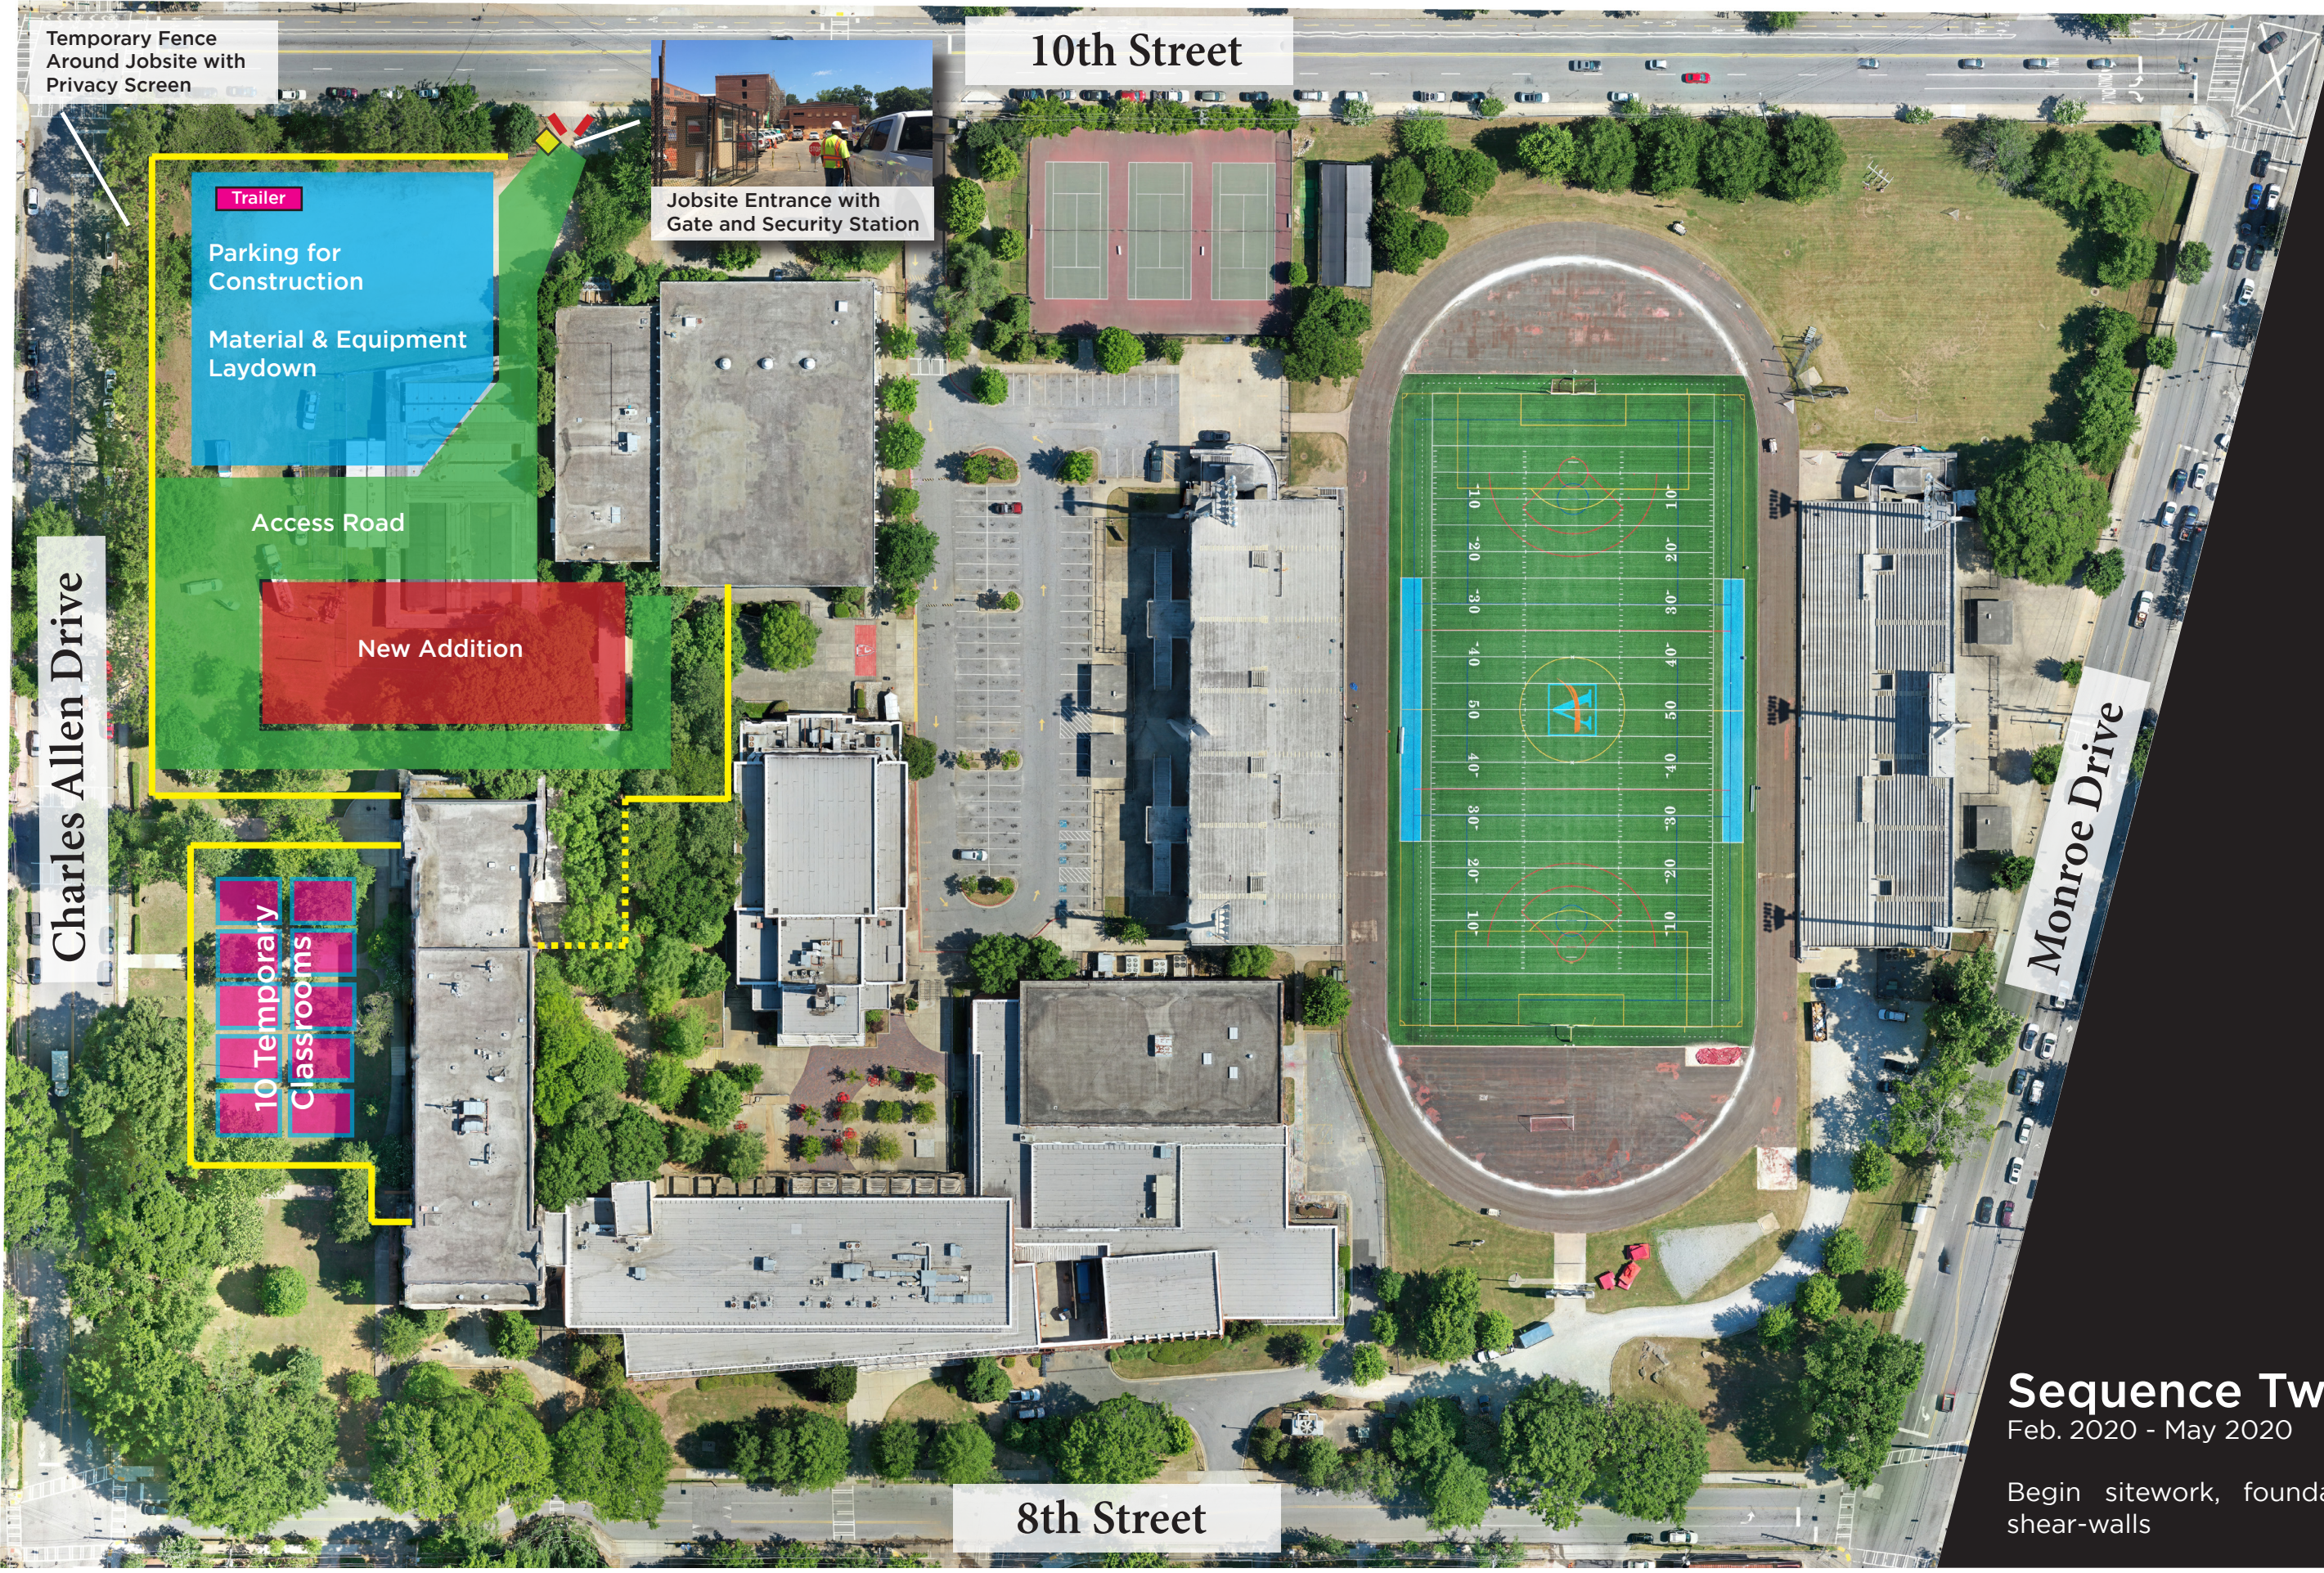

Temporary Fence
Around Jobsite with
Privacy Screen

Charles Allen Drive

10 Temporary
Classrooms

Trailer

Parking for
Construction

Material & Equipment
Laydown

Access Road

New Addition

Jobsite Entrance with
Gate and Security Station


10th Street

8th Street

Monroe Drive

Sequence Two
Feb. 2020 - May 2020

Begin sitework, foundations, and
shear-walls

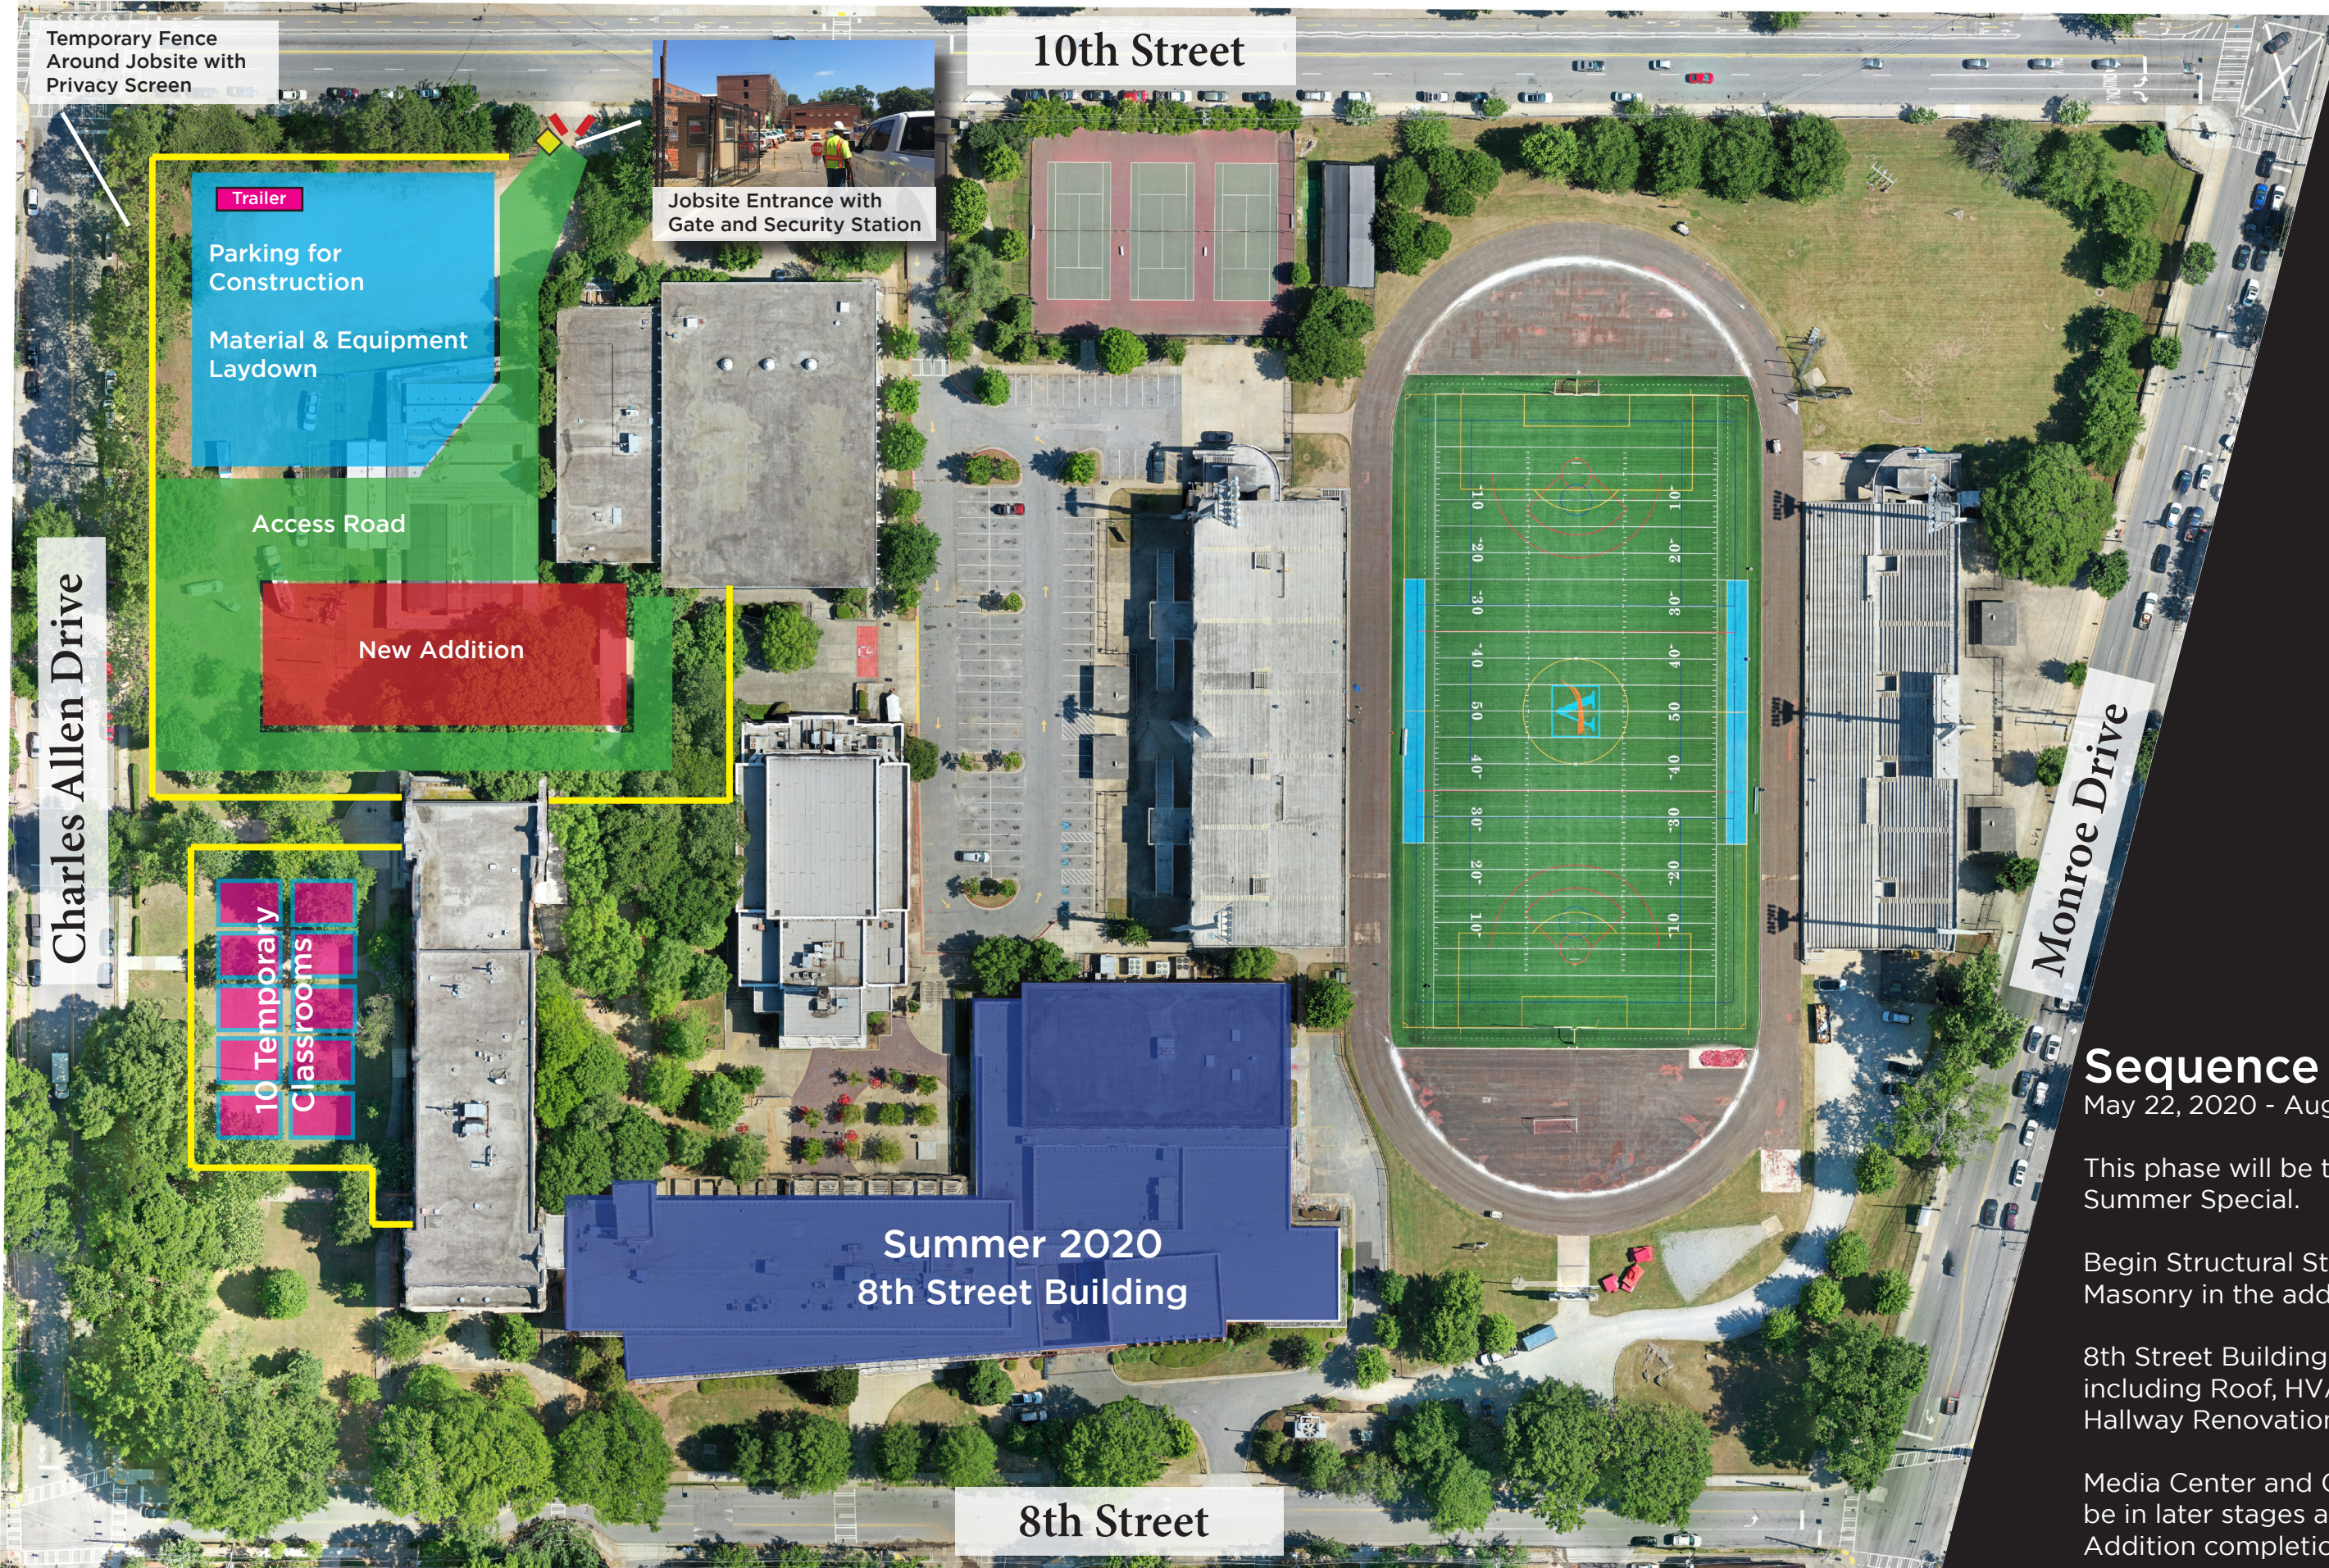

Temporary Fence
Around Jobsite with
Privacy Screen

Charles Allen Drive

Trailer

Parking for
Construction

Material & Equipment
Laydown

Access Road

New Addition

10 Temporary
Classrooms

Jobsite Entrance with
Gate and Security Station

10th Street

Summer 2020
8th Street Building

8th Street

Monroe Drive

Sequence Three


May 22, 2020 - Aug. 1, 2020

This phase will be the first
Summer Special.

Begin Structural Steel and
Masonry in the addition

8th Street Building Renovation
including Roof, HVAC and
Hallway Renovations.

Media Center and Cafeteria will
be in later stages after the New
Addition completion.

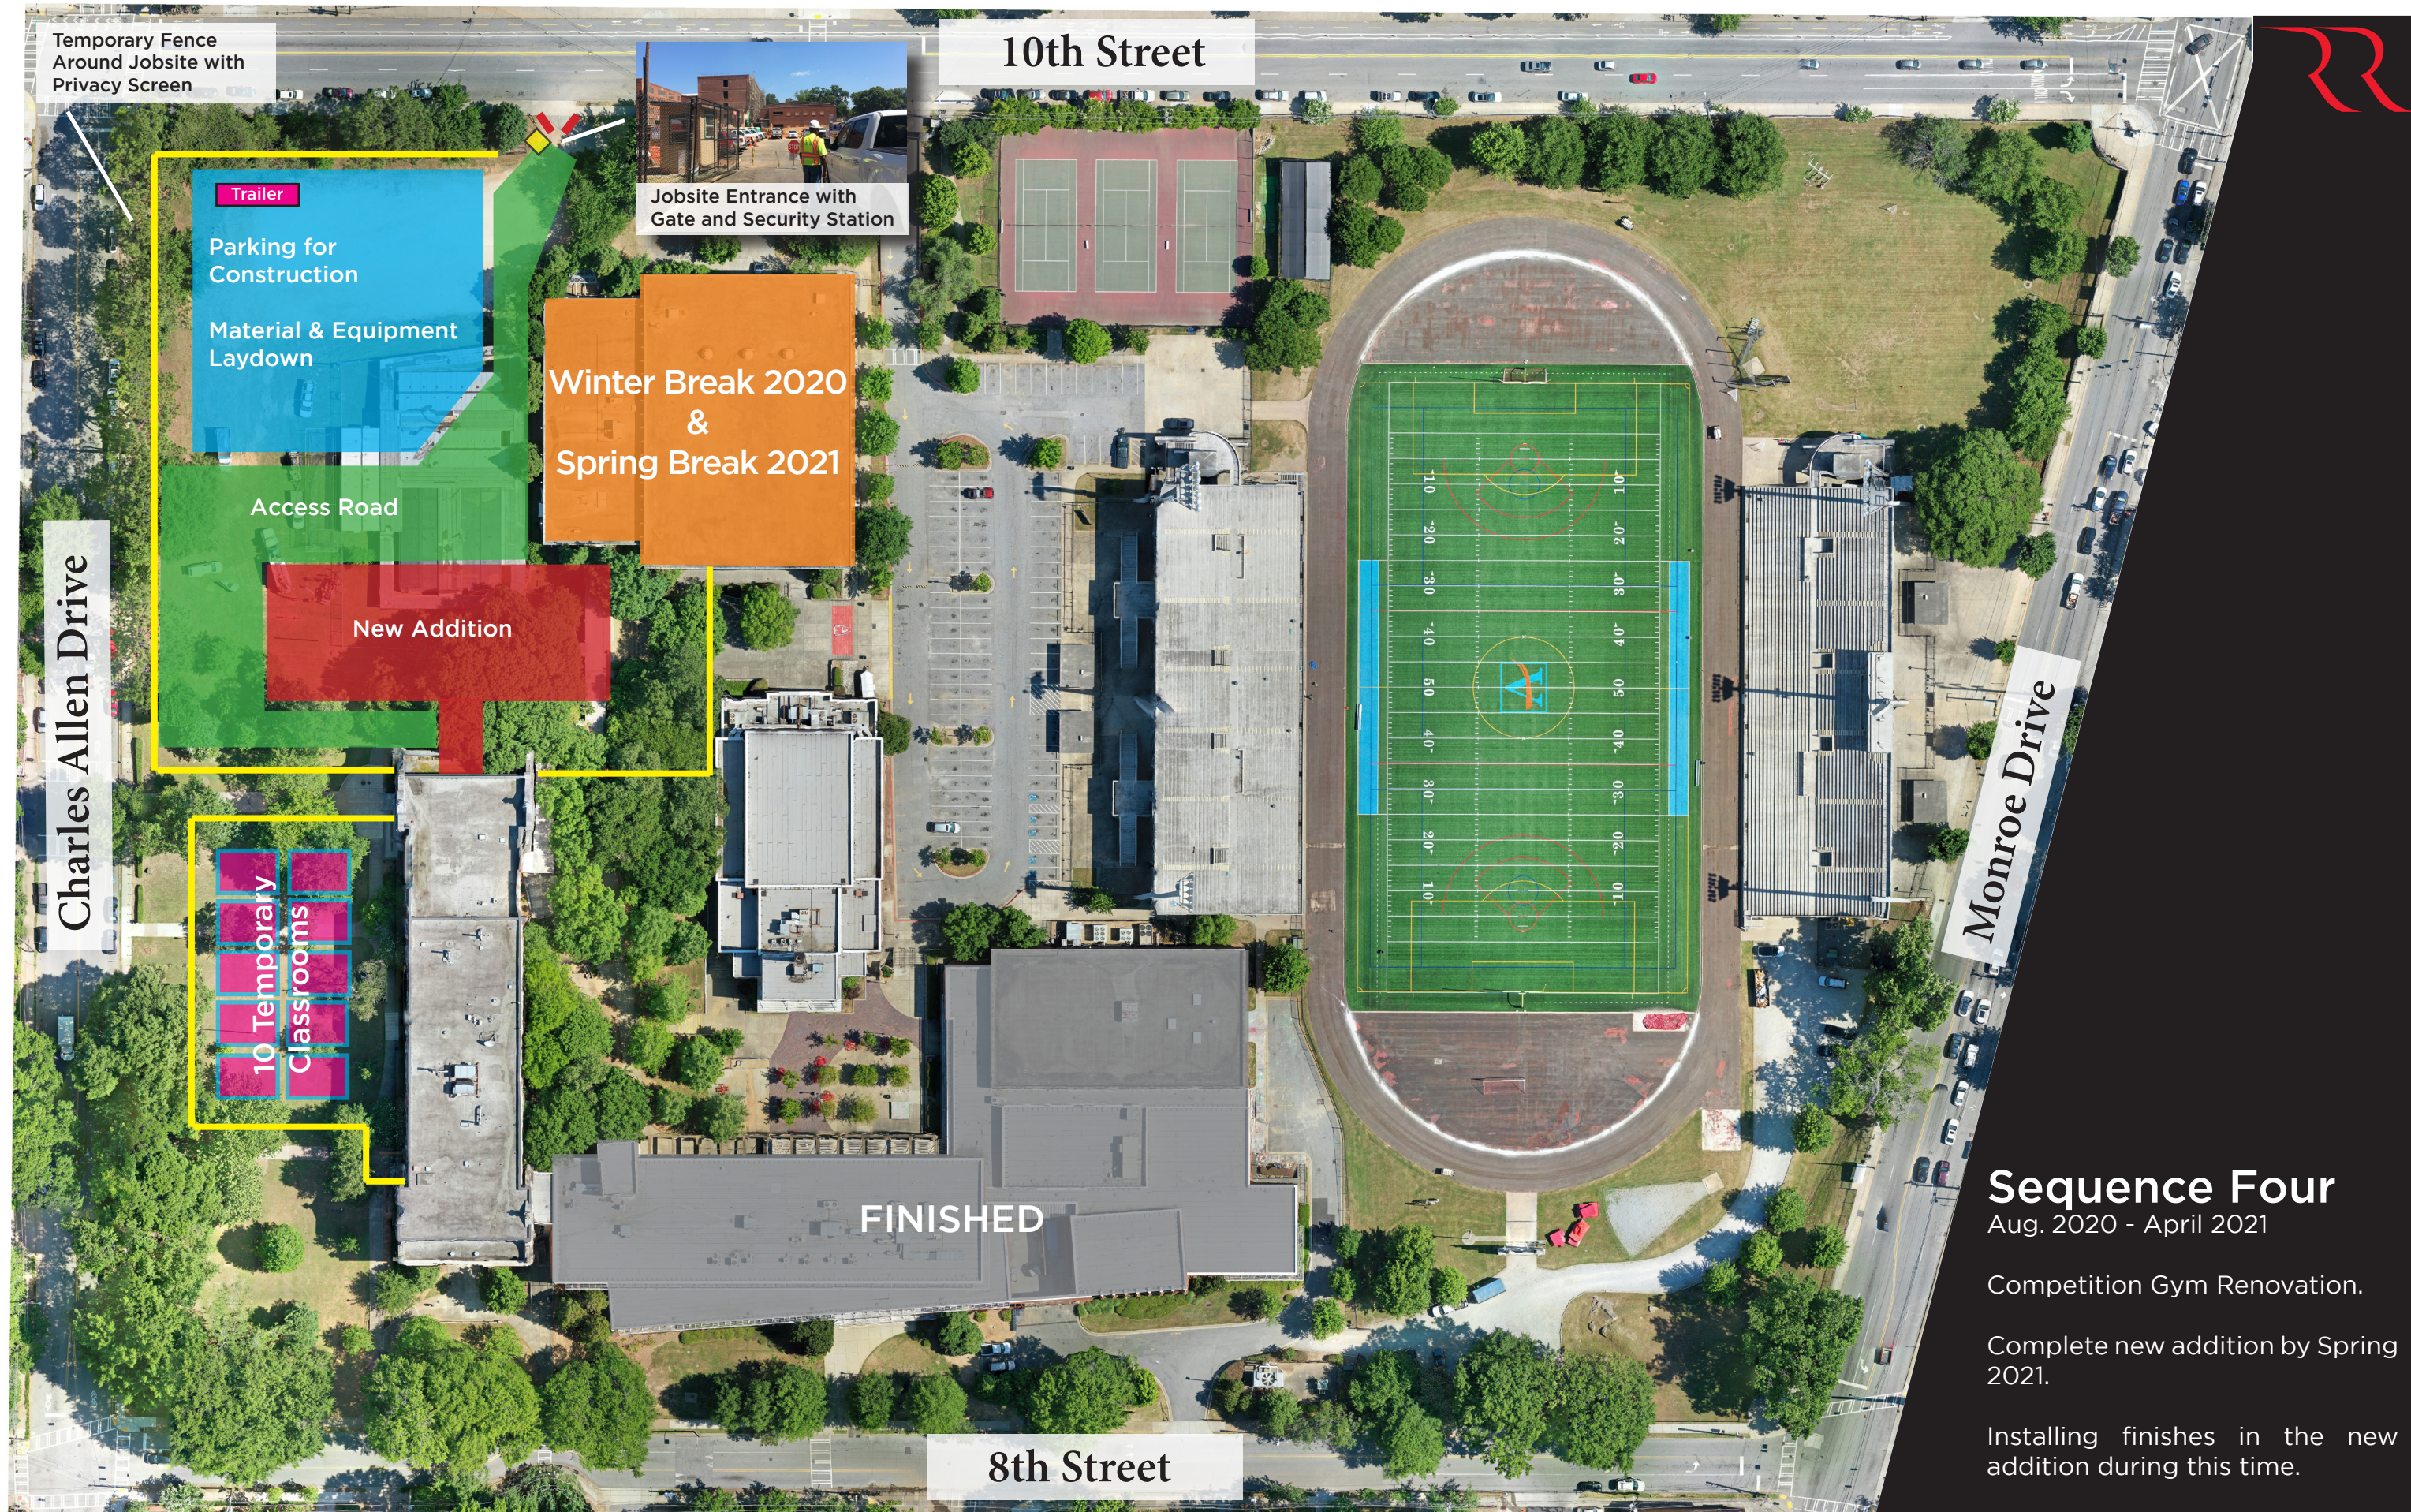


Sequence Four

Aug. 2020 - April 2021

Competition Gym Renovation.

Complete new addition by Spring 2021.

Installing finishes in the new addition during this time.

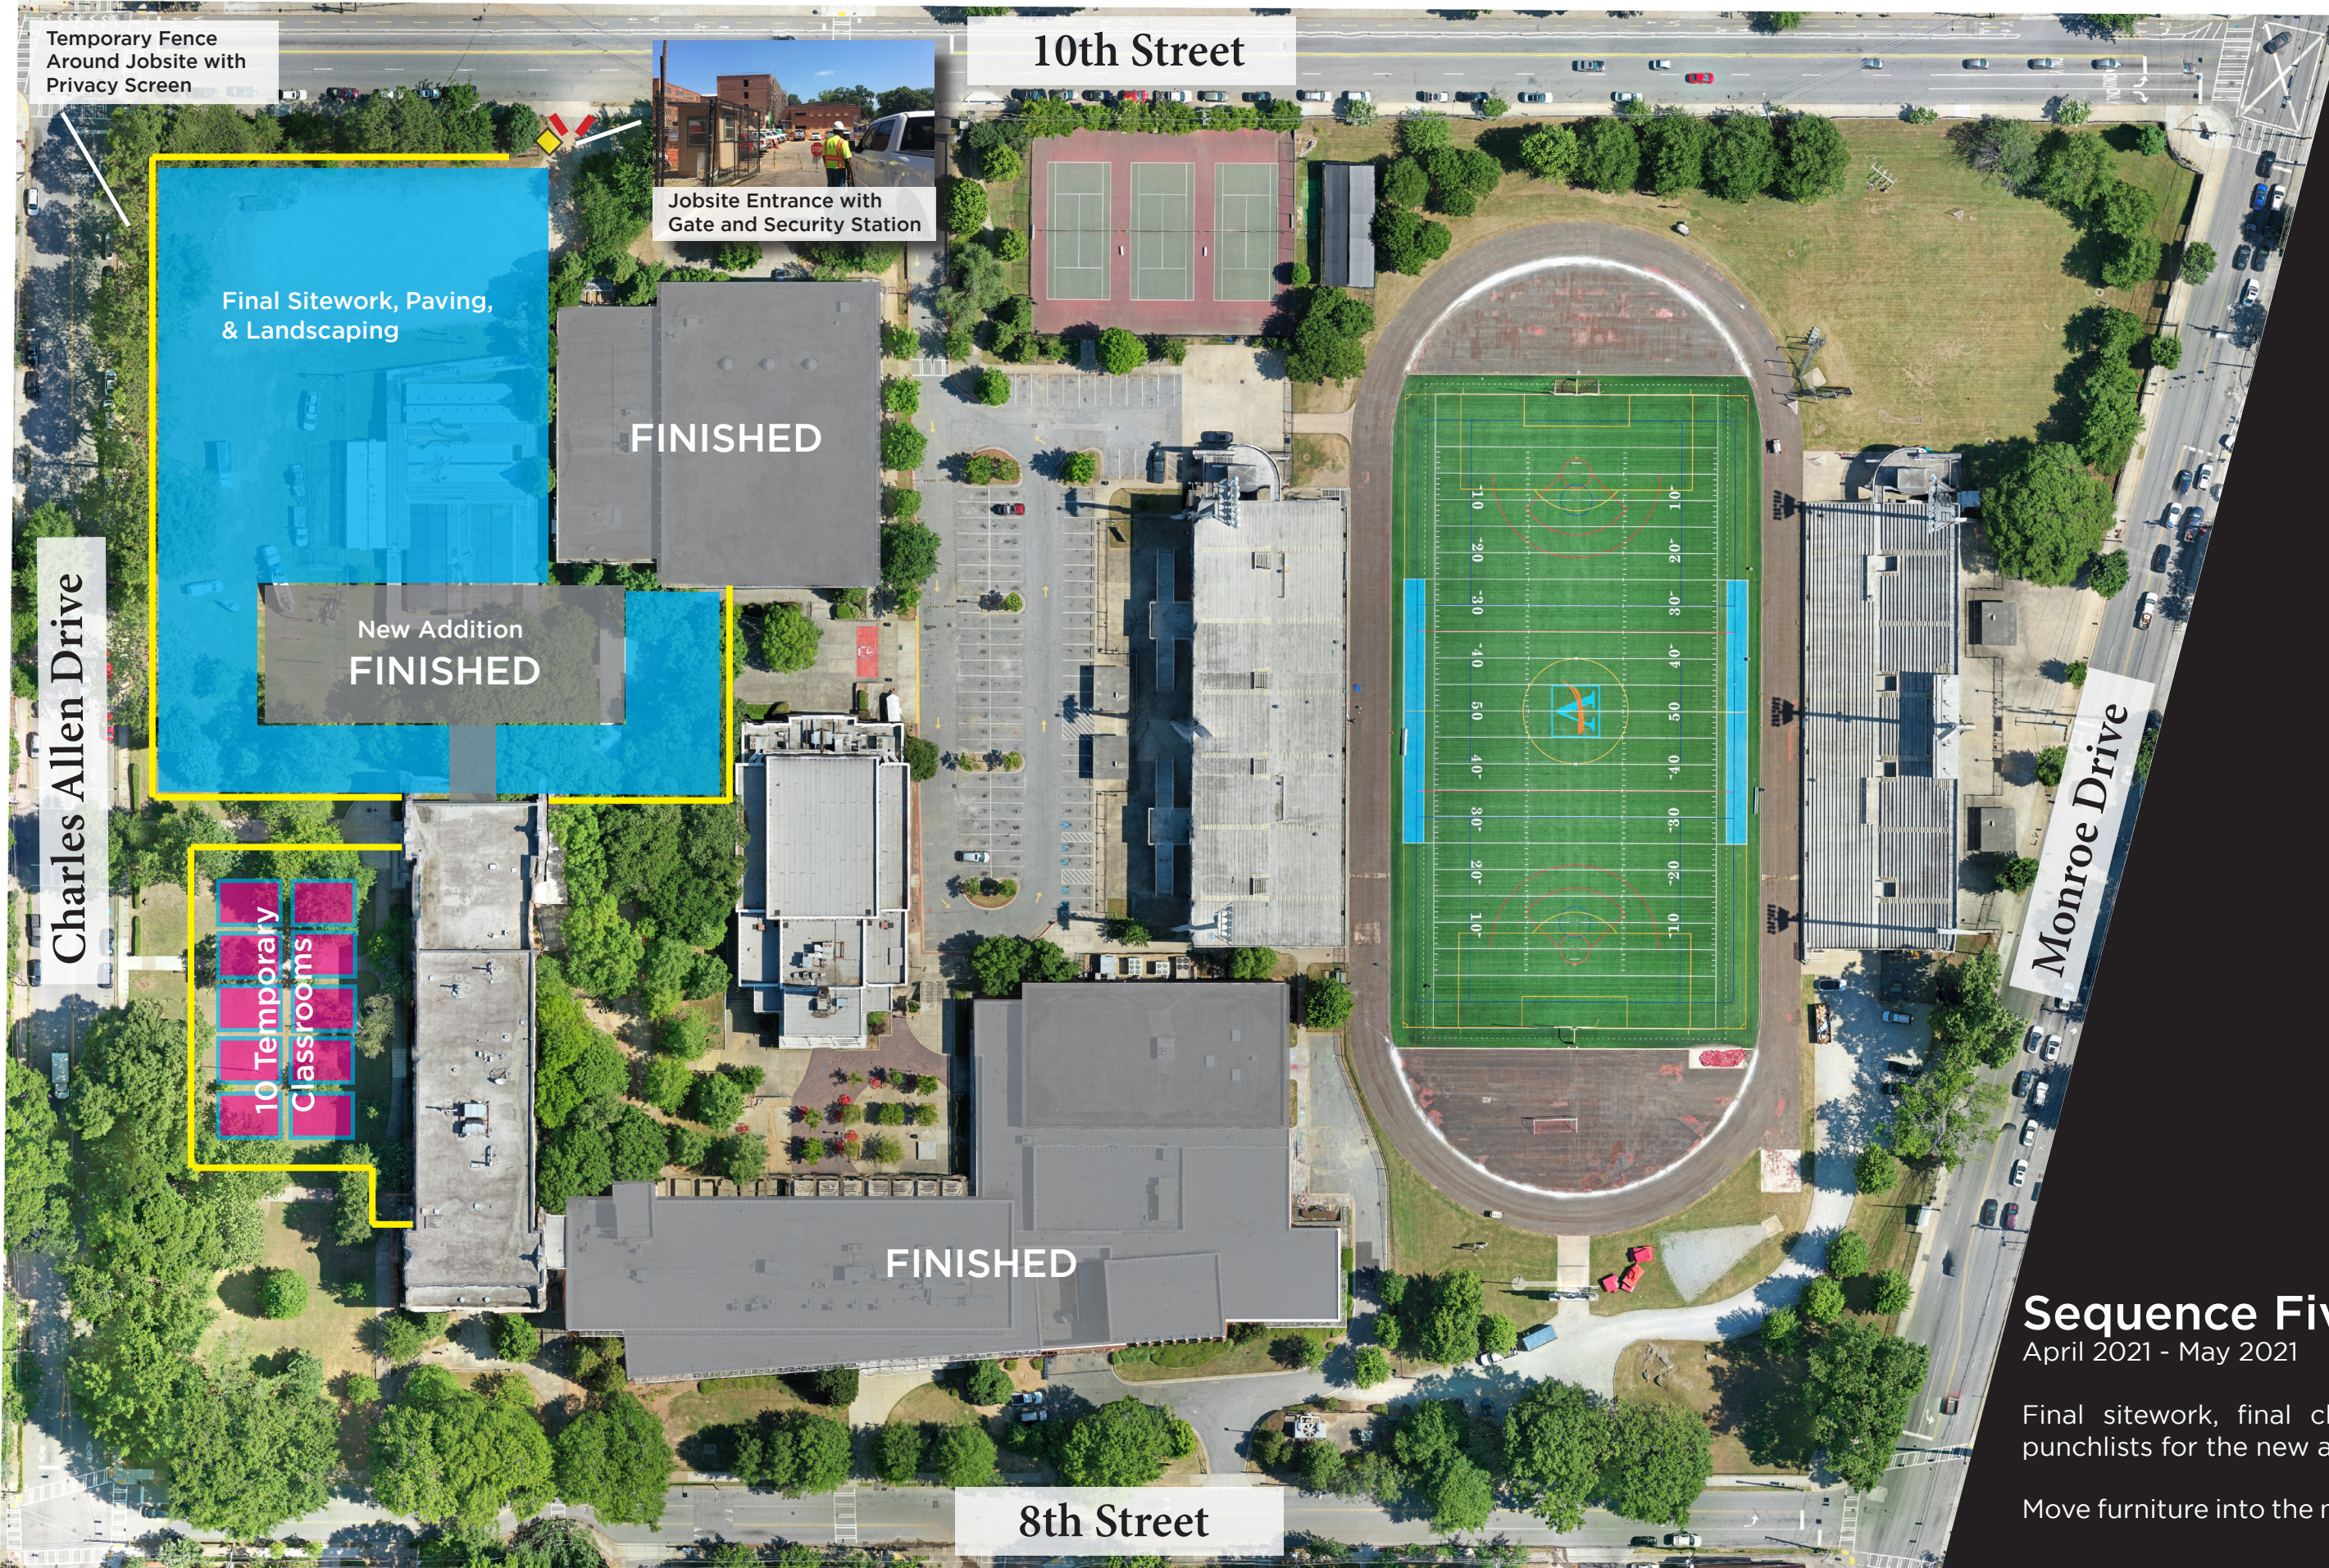

Temporary Fence
Around Jobsite with
Privacy Screen

Charles Allen Drive

10th Street

Jobsite Entrance with
Gate and Security Station

Final Sitework, Paving,
& Landscaping

FINISHED

New Addition
FINISHED

10 Temporary
Classrooms

FINISHED

8th Street


Monroe Drive

Sequence Five

April 2021 - May 2021

Final sitework, final cleaning, and
punchlists for the new addition.

Move furniture into the new addition.

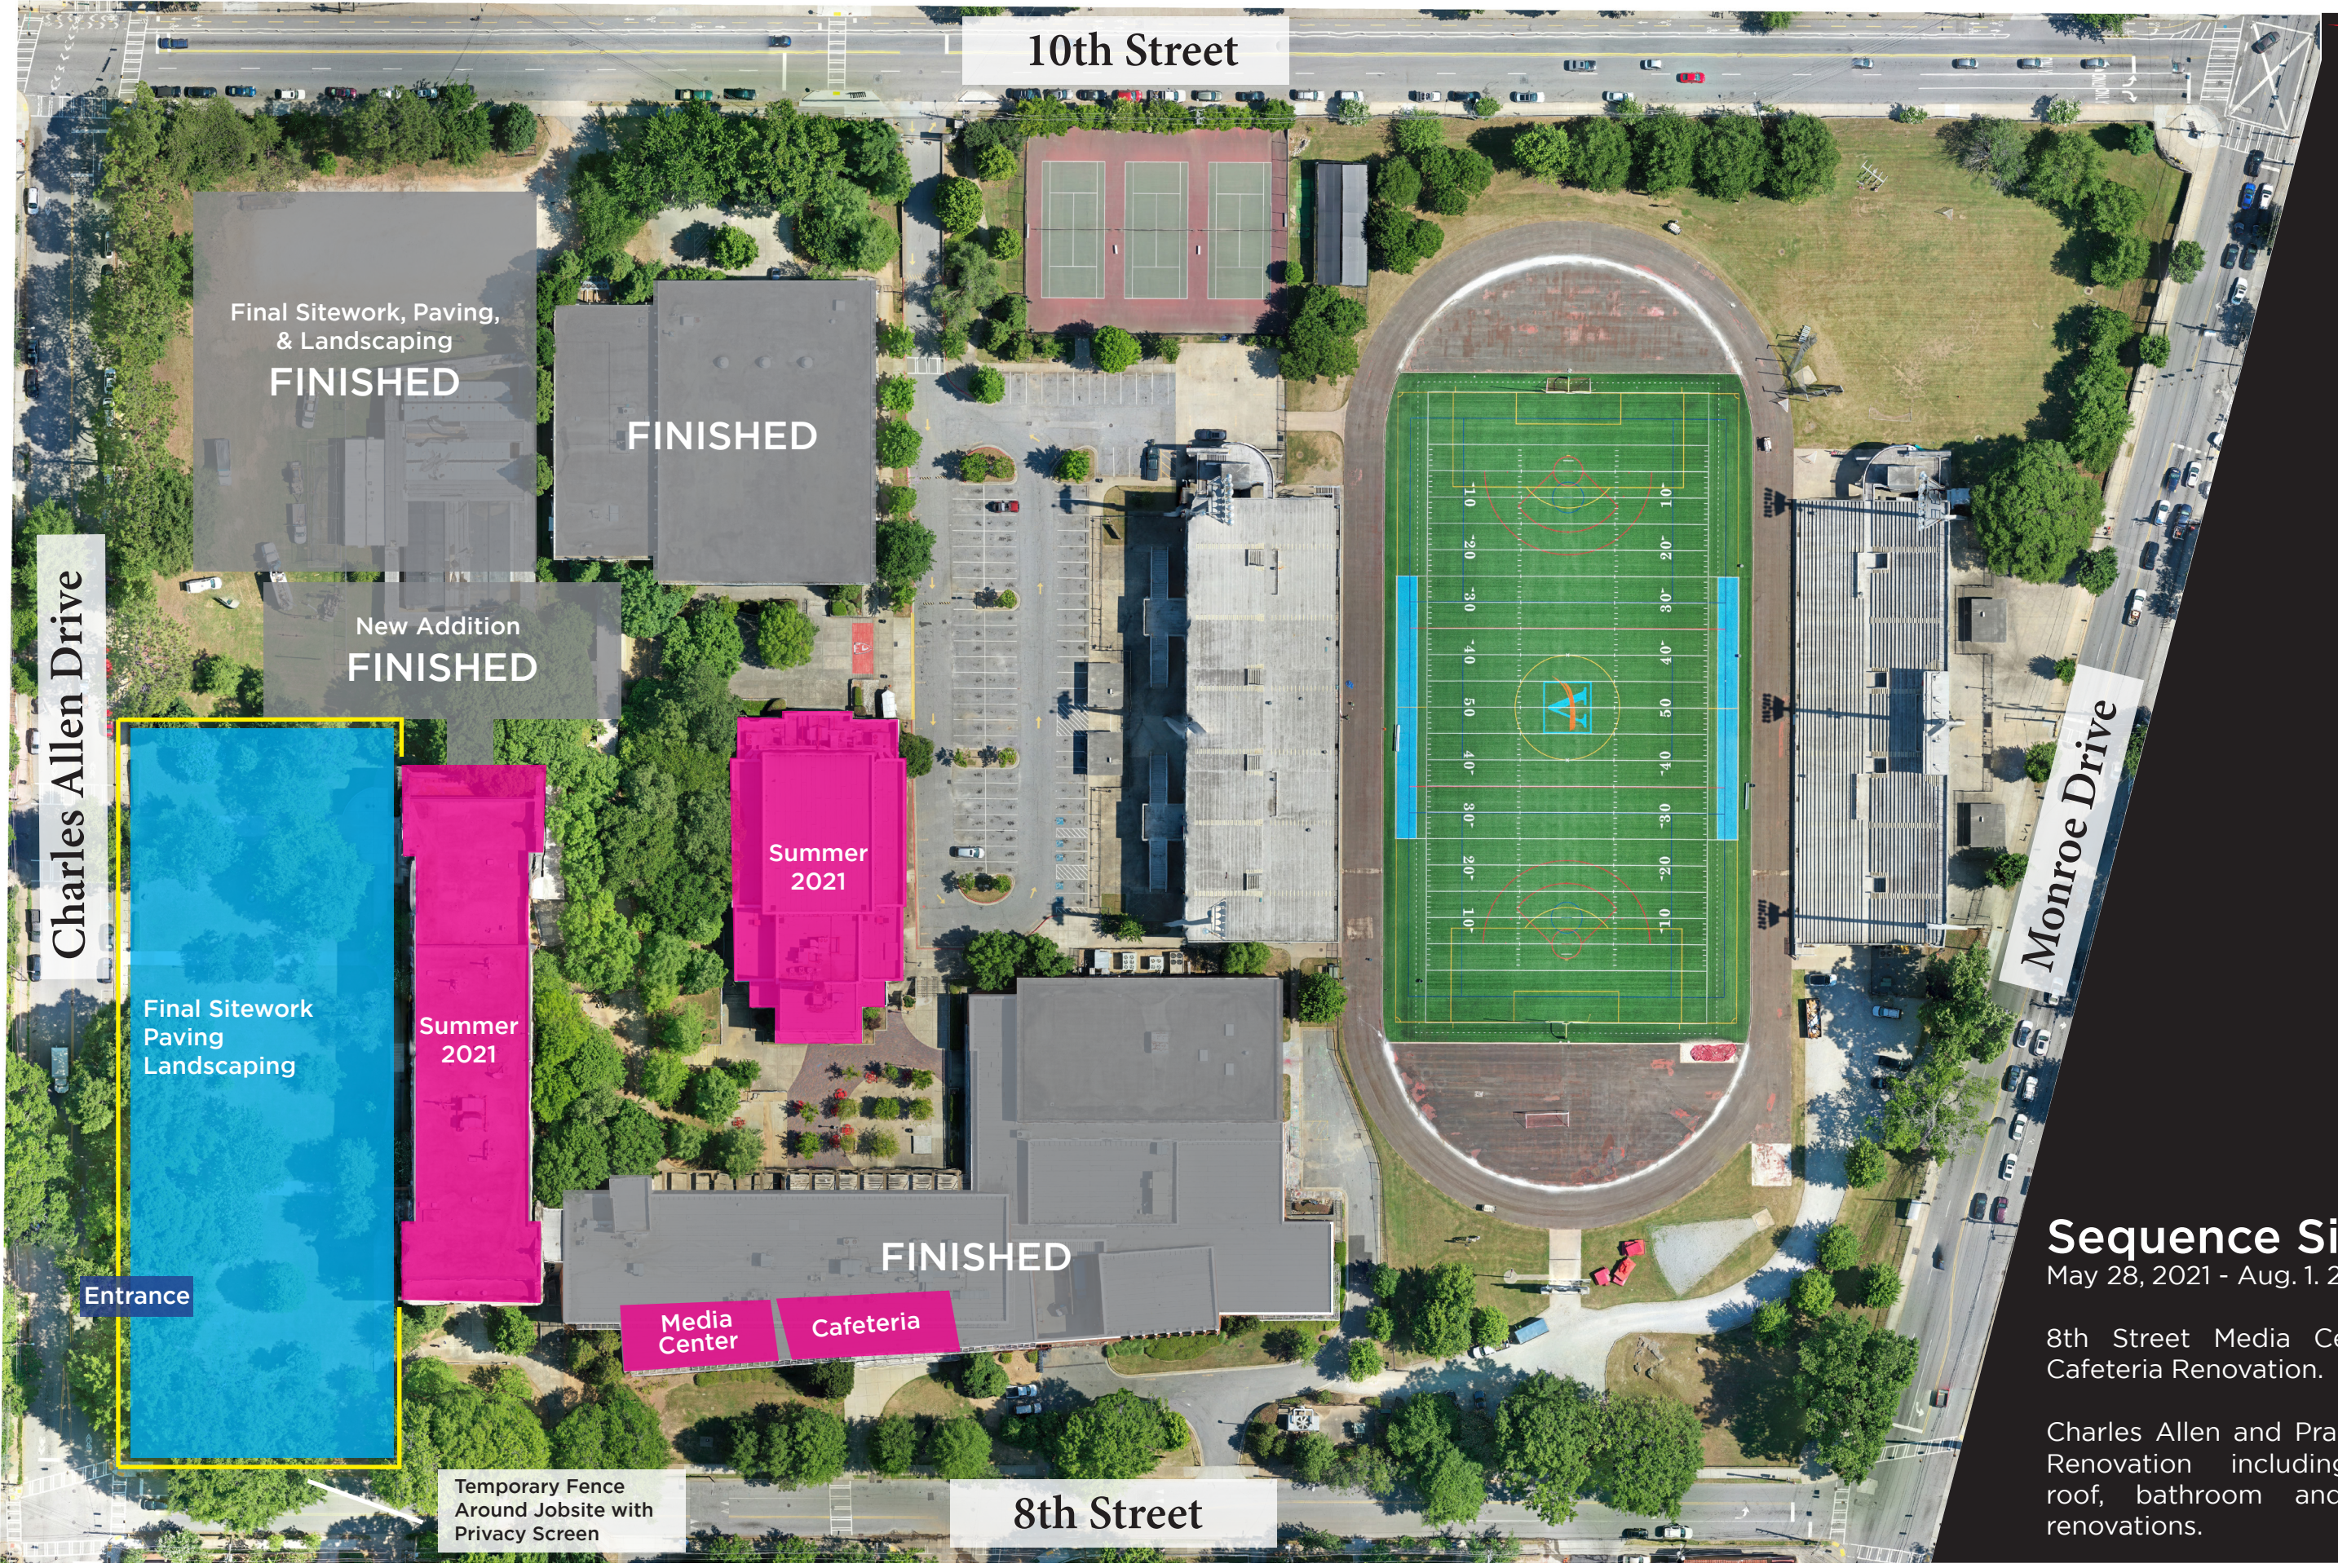

May 28, 2021 - Aug. 1. 2021

Charles Allen and Practice Gym
Renovation including HVAC,
roof, bathroom and hallway
renovations.
